


Date : 05/18/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 05/18/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 94484
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 05/18/2026 16:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the wall contractor continue backfilling at the north side bridge abutment. Retests and additional density tests were performed using a Troxler Nuclear gauge model 3430, serial no. 91643. The grading contractor hauled in suitable drier materials from an off-site borrow. Compaction results were in compliance with project requirements. The drier imported materials are being mixed with onsite wet materials, and a new proctor is being performed on the blended materials.


We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

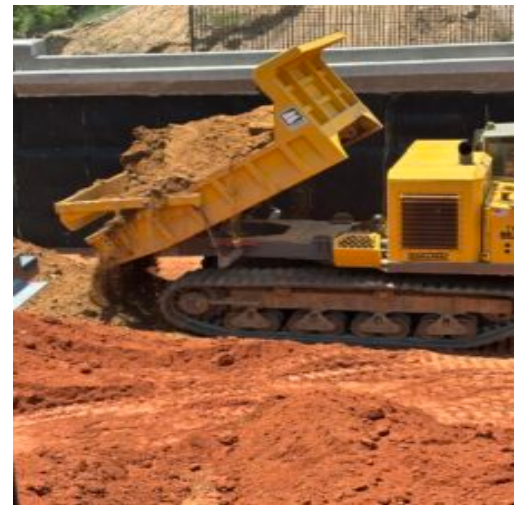

Placing and mixing onsite fill materials and performing density tests using a Troxler Nuclear gauge

Date : 05/18/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 05/18/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 94484
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 05/18/2026 16:30
ASEC Technician Name : Clyde Smith

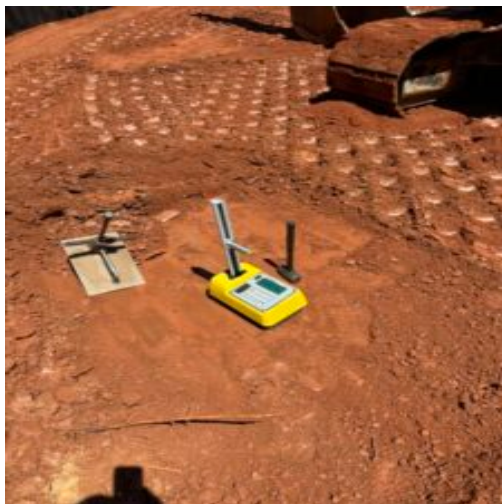

Date : 05/18/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 05/18/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 94484
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 05/18/2026 16:30
ASEC Technician Name : Clyde Smith



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
