

Date : 05/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 05/20/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 94632
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 05/20/2026 17:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the wall contractor continue backfill for the north side bridge abutment. The grading contractor continued to haul in suitable fill that was placed in compacted lifts. The fill placement was visually observed by probing using a rounded end steel rod and appeared to be compacted suitable for requirements of 95%. Onsite stockpile materials were placed and compacted at outside wing walls in non-structural areas.

The writer also continued observing subgrade soils being undercut for the drive entrance to Seven Hills, 4 lots, phase 13. The subgrade soils observed were probed using a rounded end steel rod which appeared stable and was approved for base stone placement.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.




Fill placement and observation at north side bridge abutment. The compacting efforts were suitable for specifications.



Date : 05/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 05/20/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 94632
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 05/20/2026 17:30
ASEC Technician Name : Clyde Smith

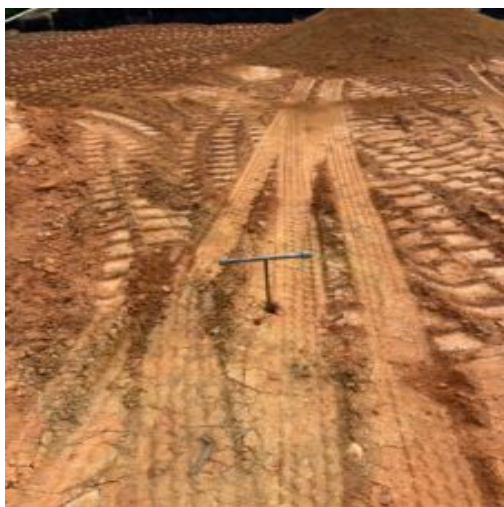

Areas which was probed with deep penetration was re rolled to satisfied recommendations.

Date : 05/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 05/20/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 94632
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 05/20/2026 17:30
ASEC Technician Name : Clyde Smith



Subbase and sub grade observed at entrance to
Seven Hills phase 13

Date : 05/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 05/20/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 94632
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 05/20/2026 17:30
ASEC Technician Name : Clyde Smith



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
