

Date : 05/12/2026
Project No : 2025C216
Client Company : Artisan
Arrival Time : 05/12/2026 9:00
Onsite Hours : 03:00

ASEC Report ID : 94216
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : clear and sunny
Departure Time : 05/12/2026 12::0
ASEC Technician Name : Narayana Ganesh Undavalli


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The contractor excavated soil using a PC 210 LC excavator and placed pipe of diameter 8 inches and 77 lineal feet between the manholes. Fill material was placed in lifts, spread using a crawler bulldozer, and compacted using both a sheep-foot roller and a Caterpillar 815. Density tests were performed, and the results met the required project compaction specifications.

On the other side, the crew continued working on the deceleration lane, where the subgrade was leveled, and fill material was placed in lifts using a crawler bulldozer and compacted using a sheep-foot roller.


At the Naturewalk neighborhood site, the crew continued trench excavation using a hydraulic excavator equipped with a rock grinder to achieve the required depth and width.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

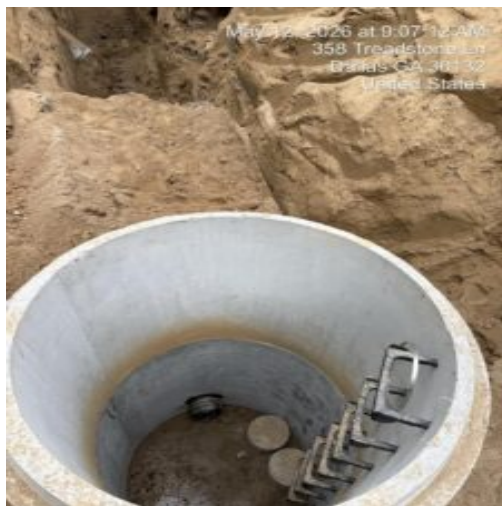

Date : 05/12/2026
Project No : 2025C216
Client Company : Artisan
Arrival Time : 05/12/2026 9:00
Onsite Hours : 03:00

ASEC Report ID : 94216
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : clear and sunny
Departure Time : 05/12/2026 12::0
ASEC Technician Name : Narayana Ganesh Undavalli

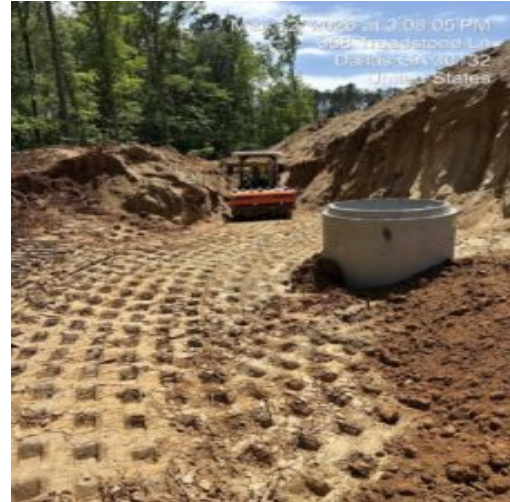

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
