


Date : 05/12/2026
Project No : 2025C216
Client Company : Artisan
Arrival Time : 05/12/2026 08:00
Onsite Hours : 04:00

ASEC Report ID : 94358
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : sunny
Departure Time : 05/12/2026 12:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Work started working between manholes B18 and B19 by excavating the trench to the required depth beginning at Manhole B18. After the trench bottom was leveled and prepared, the crew installed approximately 120 feet of 8-inch PVC pipe toward manhole B19 while maintaining the required alignment and grade. Following the pipe installation, backfill material was placed in lifts around the pipe and within the trench. The first two lifts, approximately 6 to 8 inches thick, were compacted using a trench compactor. Additional lifts of backfill material were then placed and compacted using a mini sheep-foot roller to compact throughout the trench.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

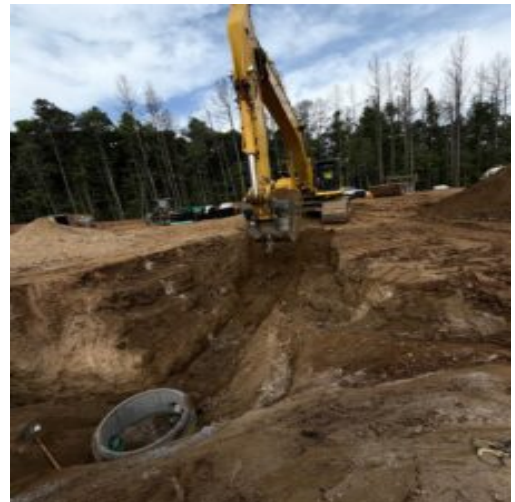

Date : 05/12/2026
Project No : 2025C216
Client Company : Artisan
Arrival Time : 05/12/2026 08:00
Onsite Hours : 04:00

ASEC Report ID : 94358
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : sunny
Departure Time : 05/12/2026 12:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
