


Date : 06/04/2026
Project No : 2025C216
Client Company : Artisan
Arrival Time : 06/04/2026 13:00
Onsite Hours : 02:00

ASEC Report ID : 95124
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : Sunny
Departure Time : 06/04/2026 15:00
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the paving contractor complete fine grading at Nature Walk Parkway and request a proof-roll of the subbase stone. The writer observed proof-rolling using a loaded tandem dump truck on subbase stone making two passes over all areas. The subbase appeared stable under traffic with no apparent movement detected and was approved for asphalt binder mix placement. The writer also observed the grading contractor continue filling in eroded rills at the unit 2 building lots.


We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

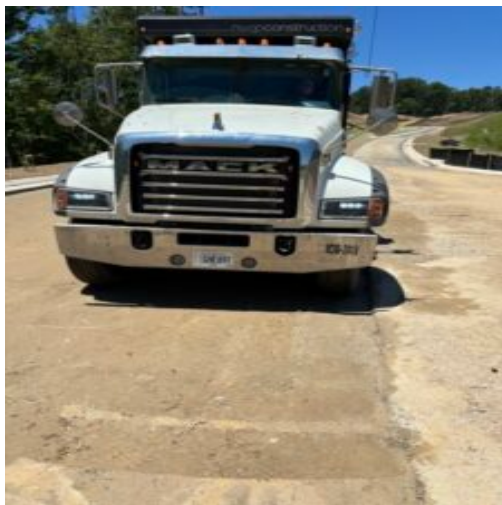

Proof rolling subbase stone at Nature Walk Pkwy. between sanitary sewer manholes #9 and 11 using a tandem dump truck with 19 tons.

Date : 06/04/2026
Project No : 2025C216
Client Company : Artisan
Arrival Time : 06/04/2026 13:00
Onsite Hours : 02:00

ASEC Report ID : 95124
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : Sunny
Departure Time : 06/04/2026 15:00
ASEC Technician Name : Clyde Smith

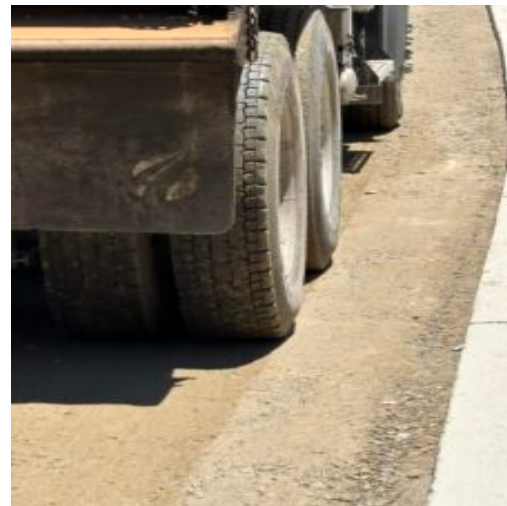

Date : 06/04/2026
Project No : 2025C216
Client Company : Artisan
Arrival Time : 06/04/2026 13:00
Onsite Hours : 02:00

ASEC Report ID : 95124
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : Sunny
Departure Time : 06/04/2026 15:00
ASEC Technician Name : Clyde Smith



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
