

Date : 10/31/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/31/2025 07:30
Onsite Hours : 08:00

ASEC Report ID : 87583
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : sunny
Departure Time : 10/31/2025 15:30
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


Excavation and installation continued today at the Cassville Road tract for the French drain ("burrito wrap") project. Work continued at the midpoint of Point C3. The crew cleared the site area and excavated the soil to the required depth. Gravel was placed at the base, followed by the installation of pipe. Additional gravel was placed on top of the pipe, then covered with plastic sheeting. The trench was backfilled with soil and compacted. No groundwater or slope instability was observed at the time of excavation.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 10/31/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/31/2025 07:30
Onsite Hours : 08:00

ASEC Report ID : 87583
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : sunny
Departure Time : 10/31/2025 15:30
ASEC Technician Name : Samara Simha Reddy Kandi

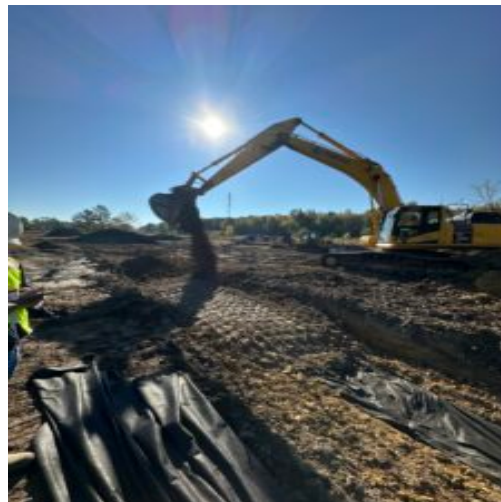

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
