

Date : 05/13/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 05/13/2026 8
Onsite Hours : NaN:00

ASEC Report ID : 94504
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : clear and sunny
Departure Time : 05/13/2026 3
ASEC Technician Name : Narayana Ganesh Undavalli


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The contractor continued working on Lots #A12, B8, B9 and the adjacent roadway area. Fill material was placed in lifts, spread using a crawler bulldozer, and compacted using both a sheep-foot roller and a Caterpillar 815. Density tests were performed, and the results met the required project compaction specifications.

Contractor continued working on the Naturewalk Parkway roadside slope. Fill material was placed in lifts, spread using a crawler bulldozer and compacted using a caterpillar 815. Density tests were performed and the results met the required project compaction specifications.


At the Naturewalk neighborhood site, the crew continued trench excavation using a hydraulic excavator equipped with a rock grinder to achieve the required depth and width.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

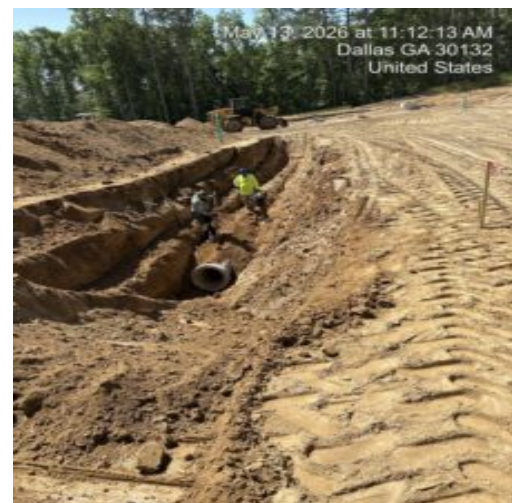

Date : 05/13/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 05/13/2026 8
Onsite Hours : NaN:00

ASEC Report ID : 94504
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : clear and sunny
Departure Time : 05/13/2026 3
ASEC Technician Name : Narayana Ganesh Undavalli

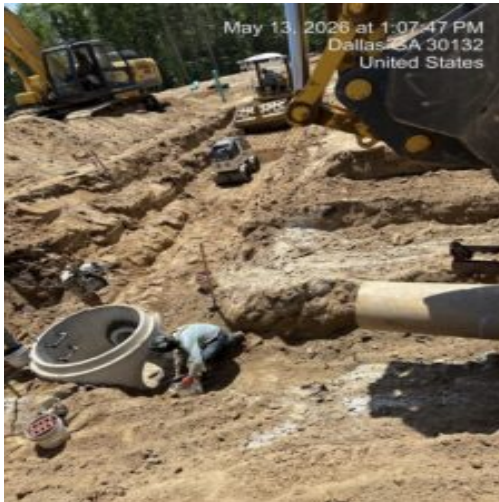

Date : 05/13/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 05/13/2026 8
Onsite Hours : NaN:00

ASEC Report ID : 94504
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : clear and sunny
Departure Time : 05/13/2026 3
ASEC Technician Name : Narayana Ganesh Undavalli



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
