

Date : 06/03/2026
Project No : 2026C125
Client Company : Lewis Contracting
Arrival Time : 06/03/2026 08:00
Onsite Hours : 04:00


ASEC Report ID : 95070
Name of the Project : Pittman Park - Garibaldi St. Stormwater
Project Location : Atlanta
Weather : sunny
Departure Time : 06/03/2026 12:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The crew continued remediation work at the northwest corner of the foundation area. The previously identified excavation error, where approximately 4 feet had been excavated inside the stake line instead of 4 feet outside the stake line as required by the plans, was addressed. The excavation limits were corrected by re-excavating the area to the proper location and dimensions, and the foundation footprint was re-established based on the stake offsets shown in the wall detail drawings.

In addition, water that had accumulated at the opposite corner of the foundation area was pumped out to provide suitable working conditions. The affected areas were then reworked, and additional excavation was performed as necessary to achieve the required plan dimensions. The sub-grade was trimmed and leveled in preparation for continuation of the foundation construction activities.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

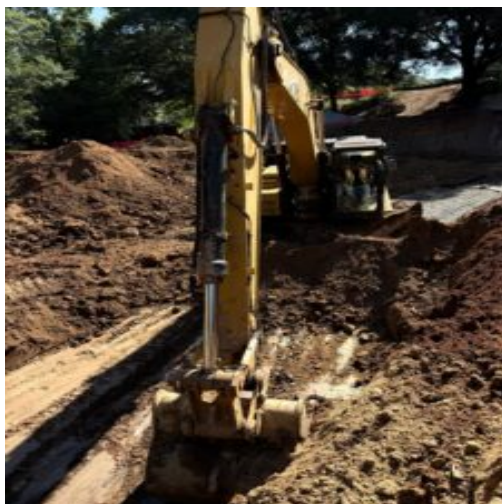

Date : 06/03/2026
Project No : 2026C125
Client Company : Lewis Contracting
Arrival Time : 06/03/2026 08:00
Onsite Hours : 04:00

ASEC Report ID : 95070
Name of the Project : Pittman Park - Garibaldi St. Stormwater
Project Location : Atlanta
Weather : sunny
Departure Time : 06/03/2026 12:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
