



Date : 05/01/2026
Project No : 2026C133
Client Company : Artisan
Arrival Time : 05/01/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 93870
Name of the Project : Salacoa (AKA Boone Ford Rd) Robert's
Dam
Project Location : Calhoun
Weather : sunny
Departure Time : 05/01/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The crew placed fill material along the dam alignment using a tandem-axled dump truck, maintaining the designed 3:1 slope configuration. The dumped material was then spread uniformly using a crawler bulldozer. The fill was placed in controlled lifts, typically 8 to 10 inches thick throughout the embankment. Each lift was compacted using a sheep-foot roller. Density tests were performed on each compacted lift which met required compaction.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

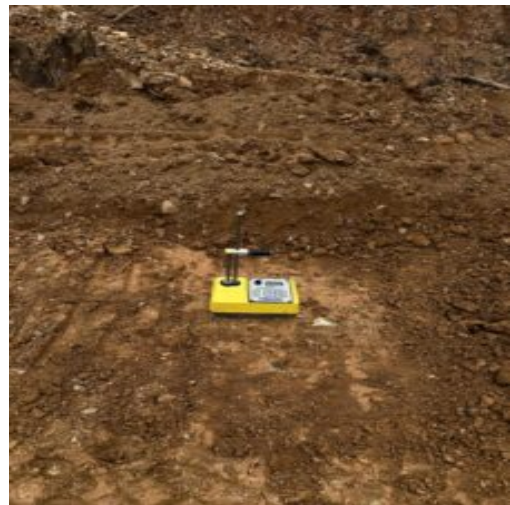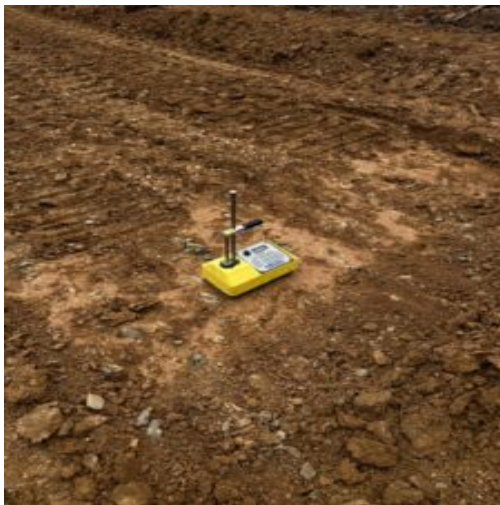

Date : 05/01/2026
Project No : 2026C133
Client Company : Artisan
Arrival Time : 05/01/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 93870
Name of the Project : Salacoa (AKA Boone Ford Rd) Robert's
Dam
Project Location : Calhoun
Weather : sunny
Departure Time : 05/01/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
