


Date : 05/22/2026
Project No : 2026C142
Client Company : KFE
Arrival Time : 05/22/2026 08:30
Onsite Hours : 02:00

ASEC Report ID : 94699
Name of the Project : Bailey Station Way
Project Location : Sharpsburg
Weather : cloudy
Departure Time : 05/22/2026 10:30
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Contractor continued placing fill material for building pad Suite 3 and near Suite 1 using dump trucks. The material was spread along Suite 3 with the help of a crawler bulldozer to achieve the required grading. No compaction activities were performed in this area during the site visit because only one worker was present on site at the time. Density tests were performed in the Suite 1 area, which had been compacted on the previous working day, and the test results met the required compaction specifications.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

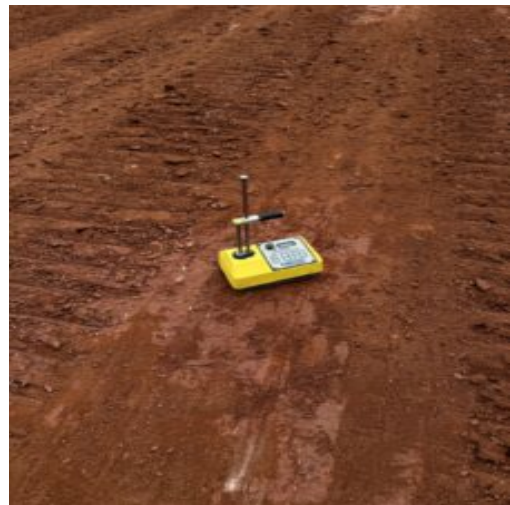

Date : 05/22/2026
Project No : 2026C142
Client Company : KFE
Arrival Time : 05/22/2026 08:30
Onsite Hours : 02:00

ASEC Report ID : 94699
Name of the Project : Bailey Station Way
Project Location : Sharpsburg
Weather : cloudy
Departure Time : 05/22/2026 10:30
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
