


Date : 12/07/2020
Project No : 2020C009
Client Company : DR Horton
Arrival Time : 12/07/2020 10:00
Onsite Hours : 04:00

ASEC Report ID : 1436
Name of the Project : Monet Gardens
Project Location : River Road at Green Pastures Way,
Ellenwood, GA
Weather : Overcast
Departure Time : 12/07/2020 14:00
ASEC Technician Name : Dave Bek

The site was visited by the undersigned AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to assure compliance with project drawings/specifications, applicable codes, and materials submittals. The following observations were made on site today:

1. On-site today @ 10:00 for general earthwork observation. Due to heavy rains the night before the resulting ground saturation levels were very high. The contractor to expedite drying spread overly saturated topsoil to various areas of the site.
2. No structural compaction was performed today.
3. Excavation work continued on sewer line A at the intersection of Green Pastures Way and River Rd.

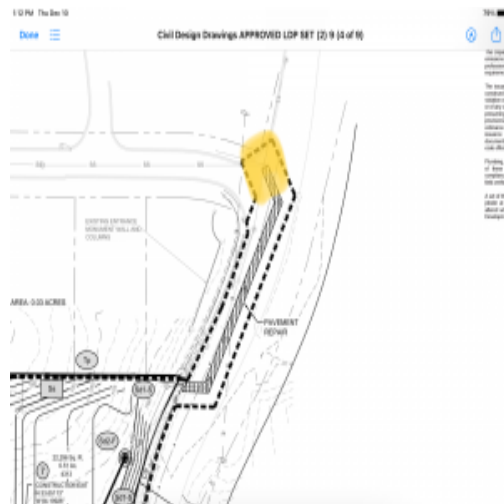

Sewer Line A at Intersection of Green Pastures Way and River Rd

Dave Bek

Senior Engineering Technician



Ramchandra R. Mogulla
GA P.E. 036021
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
