

Date : 06/10/2021
Project No : 2020C002
Client Company : Toll Bros. Inc.
Arrival Time : 06/10/2021 08:00
Onsite Hours : 9:00


ASEC Report ID : 21855
Name of the Project : Northfields at Polo Fields
Project Location : 4805 Pittman Road, Forsyth County, Georgia
Weather : Overcast
Departure Time : 06/10/2021 17:00
ASEC Technician Name : Dave Bek

The site was visited by the undersigned AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to assure compliance with project drawings/specifications, applicable codes, and materials submittals. The following observations were made on site today

Upon arrival to the site the writer observed that excavation and placement of piping from MH-BB20 to MH-BB30 and MH-BB20 to MH-BB10 continued from the previous day. Sub-grade evaluations were performed, and through visual observation and manual probing, the writer found the underlying sub-grades to be acceptable, hard red-brown silty sand w/ rock material. 6" of 57 stone was added for the bedding prior to pipe placement on both lines. Density tests were performed on the fill compaction. Based on the density test results, visual observation of the material placed and random probing of the placed lifts, the fill placed was found to be acceptable and within plan specifications.



BB20 to BB10

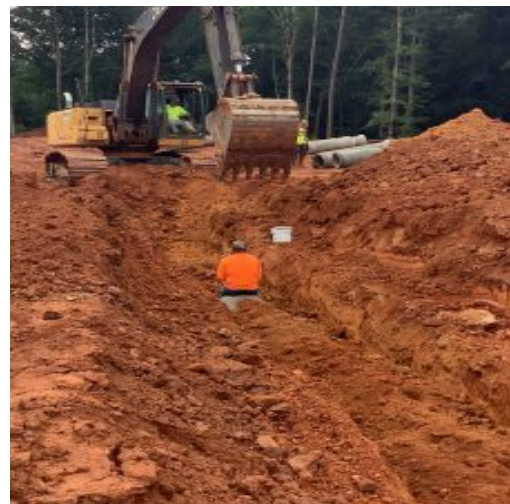

BB20 to BB30

Dave Bek

Senior Engineering Technician



Ramchandra R. Mogulla
GA P.E. 036021
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
