

Date : 07/21/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 07/21/2026 09:00
Onsite Hours : 07:00

ASEC Report ID : 96375
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 07/21/2026 16:00
ASEC Technician Name : Samara Simha Reddy Kandi


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

At CB8.7 to CB8.8, the trench had been excavated to the required depth, and installation of approximately 20 feet of 18-inch reinforced concrete pipe (RCP) was in progress at the time of observation. Between CB8.8 and CB8.9, approximately 30 feet of 18-inch RCP had been installed. Following pipe installation, approved backfill material was placed in lift around the pipe and compacted using a jumping jack compactor to provide adequate pipe support and embedment.

Elsewhere on the site, the contractor removed approximately 3 feet of saturated soil from the temporary pond area. Large boulders/rock were then placed in the excavated area to improve stability and minimize the effects of the forecasted rainfall.

Near the main roadway adjacent to the residence located at 2677 Thompson Mill Road, standing water had accumulated near the property's entrance/gate. To improve drainage in this area, the contractor installed a manhole and backfilled the excavation with onsite soil. Although the backfill material was observed to be wet, it was compacted using trench compactor. It was noted that this work was performed to address the localized drainage issue and that the area is outside the limits of the approved construction plans.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

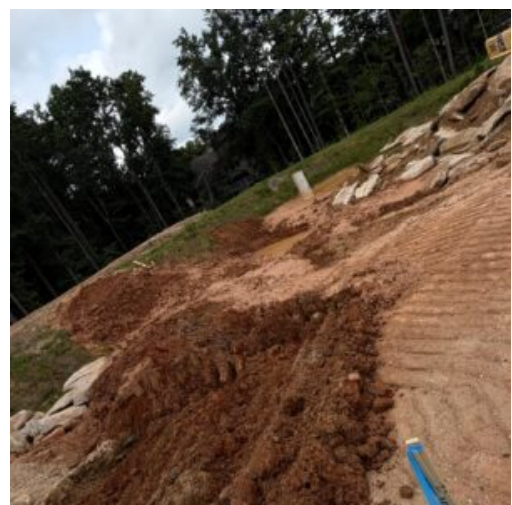

Date : 07/21/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 07/21/2026 09:00
Onsite Hours : 07:00

ASEC Report ID : 96375
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 07/21/2026 16:00
ASEC Technician Name : Samara Simha Reddy Kandi



Date : 07/21/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 07/21/2026 09:00
Onsite Hours : 07:00

ASEC Report ID : 96375
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 07/21/2026 16:00
ASEC Technician Name : Samara Simha Reddy Kandi



The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
