

Date : 07/09/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/09/2026 07:30
Onsite Hours : 08:00

ASEC Report ID : 96167
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/09/2026 15:30
ASEC Technician Name : Clyde Smith

On the above date the writer was onsite as requested and observed the Paving contractor continue placing base stone at Nature Walk Parkway between sanitary sewer manhole # 12 and 14. The writer also monitored traffic from other sub contractors traveling on existing sub grade prior to base stone being placed. The additional traffic is causing moderate rutting and scabbing with decisions being made to clip or roll down to stabilize. Additional observations will be made during proof roll of sub base stone.

The Grading contractor continues to place fill at unit 4 and phase 3, also repairing reels at eroded slope areas. The fill placement is also being monitored and tested by another technician from ASEC.



The wall contractor continued installing reinforcing steel at bridge floor slab.



Placing re steel at bridge floor slab



Blading down ruts and scabbing from additional traffic from sub contractors

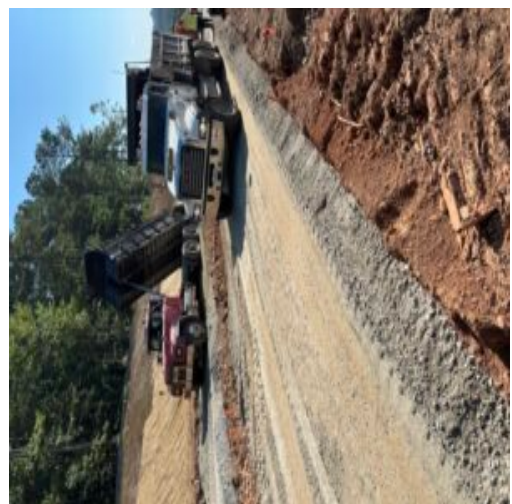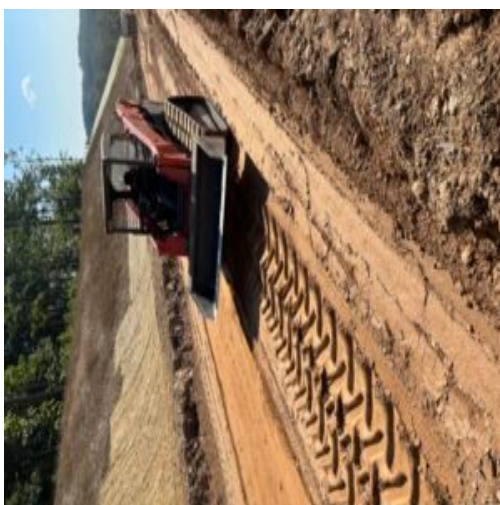

Placing sub base stone over existing sub grade

Date : 07/09/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/09/2026 07:30
Onsite Hours : 08:00

ASEC Report ID : 96167
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/09/2026 15:30
ASEC Technician Name : Clyde Smith



Additional traffic from sub contractors rutting sub grade



The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
