

Date : 07/10/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/10/2026 07:30
Onsite Hours : 08:00

ASEC Report ID : 96176
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/10/2026 15:30
ASEC Technician Name : Clyde Smith


On the above date the writer was onsite as requested and observed the Paving contractor continue to place base stone over existing sub grade at Nature Walk Parkway between sanitary sewer manholes #12 and 14. The writer continued to monitor additional traffic from sub contractors which caused additional repairs being needed on sub grade to place sub base stone.

The Grading contractor continued placing fill at unit 4 phase 3 which was monitored and tested by another technician from ASEC.

The wall contractor continued to place re steel at bridge floor slab.




Placing sub base stone and compacting

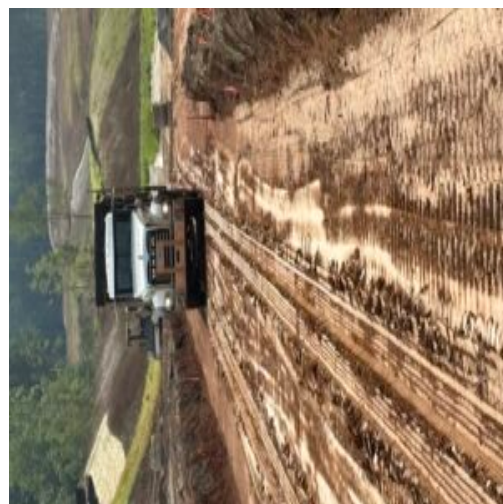

Additional sub contractors traffic on sub grade causing additional repairs needed.

Date : 07/10/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/10/2026 07:30
Onsite Hours : 08:00

ASEC Report ID : 96176
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/10/2026 15:30
ASEC Technician Name : Clyde Smith

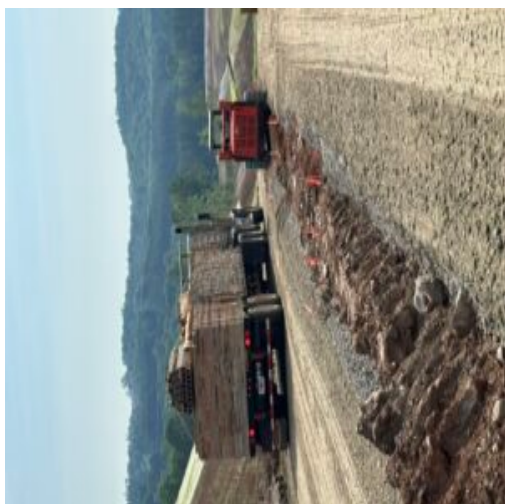

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
