

Date : 07/22/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/22/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 96359
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/22/2026 16:30
ASEC Technician Name : Clyde Smith

On the above date the writer was onsite as requested and observed the Curbing contractor begin pouring curbing (type 2) at roadway to culdesac at Seven Hills phase 13 until curbing machine broke and pour ended. The contractor continued pouring sidewalk on Seven Hills Boulevard.


The writer also assisted in observing concrete placement at bridge cart path ,raised island and north side curbing. Also observing installation of tension rods attached to dead man footing wall.

The writer also observed the Paving contractor(NWGP) continue sub grade prep. at Nature Walk Pkwy. end of Phase 1. The sub grade was clipped an extra -4" to removed saturated sub grade soils as recommended. The contractor placed additional base stone that was clipped from existing sub base previous placed. Also performed additional density checks on in place binder asphalt mix at Nature Walk pkwy. intersection to Phase 1B and 1B roadway. The writer also set up a meeting with NWGP asphalt group to discuss discrepancies at previous placed asphalt binder mix. Several density check readings were below a required compaction effort of 92% based on an estimated theoretical value of 154.0 No actual value was provided. Readings: 142.5, 140.6, 151.2, 144.8, 137.4, 133.2, 130.4, 127.7 and 141.6.

The writer also observed the Grading contractor continue hammering residual rock at building lots.



Pouring curbing at Phase 13 prior to break down

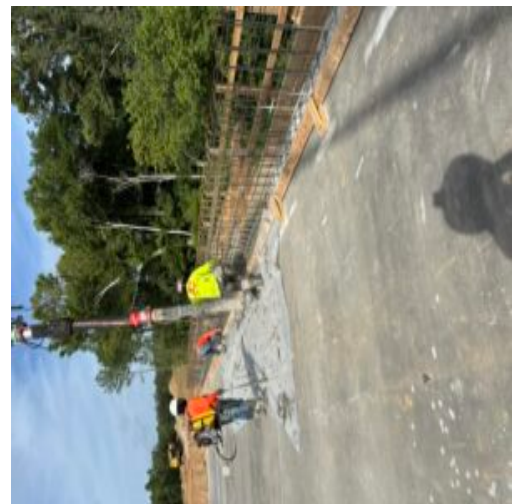

Pouring curb side at bridge

Date : 07/22/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/22/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 96359
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/22/2026 16:30
ASEC Technician Name : Clyde Smith



Poured curb at Phase 13



Density checks at Nature Walk previous binder
asphalt mix placement



Date : 07/22/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/22/2026 07:30
Onsite Hours : 9:00


ASEC Report ID : 96359
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/22/2026 16:30
ASEC Technician Name : Clyde Smith



Sub grade observations at Nature Walk end of Phase
1

Date : 07/22/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/22/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 96359
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 07/22/2026 16:30
ASEC Technician Name : Clyde Smith

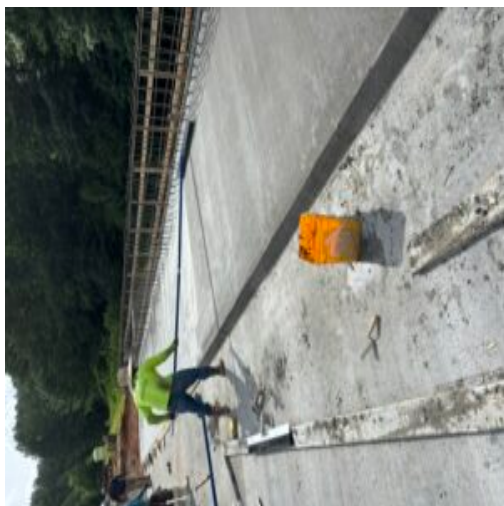

Poured Path cart at bridge

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
