

Date : 07/10/2026
Project No : 2026C100
Client Company : Artisan
Arrival Time : 07/10/2026 11:00
Onsite Hours : 04:00

ASEC Report ID : 96091
Name of the Project : Naturewalk PHASE 3 (PH 2 Extension)
Lots
Project Location : Dallas
Weather : sunny
Departure Time : 07/10/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

At the future lot areas, the crew continued fill placement operations. Fill material was delivered using articulated dump trucks, spread and leveled in lifts using a crawler bulldozer, and compacted using a sheepsfoot roller. I observed the placement and compaction activities and performed in-place density testing on the compacted fill at selected locations. The density test results met the required compaction criteria at the locations tested.


At the roadway, in-place density tests were performed at selected locations. The test results met the required compaction criteria at some locations but did not meet the requirements at other locations. The crew was advised to rework and recompact the failed areas. Follow-up density testing will be required on the next working day to verify that the corrected areas meet the required compaction criteria.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 07/10/2026
Project No : 2026C100
Client Company : Artisan
Arrival Time : 07/10/2026 11:00
Onsite Hours : 04:00

ASEC Report ID : 96091
Name of the Project : Naturewalk PHASE 3 (PH 2 Extension)
Lots
Project Location : Dallas
Weather : sunny
Departure Time : 07/10/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

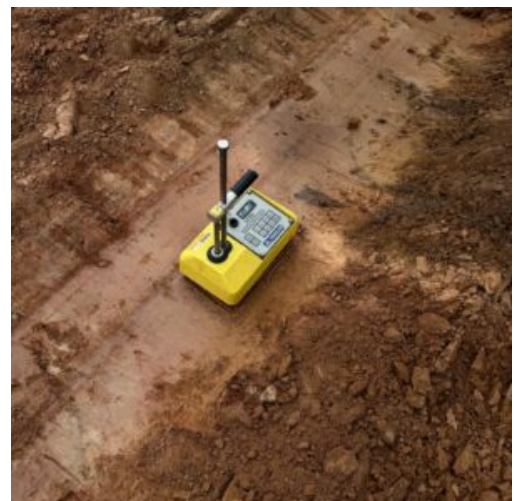

Date : 07/10/2026
Project No : 2026C100
Client Company : Artisan
Arrival Time : 07/10/2026 11:00
Onsite Hours : 04:00

ASEC Report ID : 96091
Name of the Project : Naturewalk PHASE 3 (PH 2 Extension)
Lots
Project Location : Dallas
Weather : sunny
Departure Time : 07/10/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
