

Date : 06/26/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 06/26/2026 07:30
Onsite Hours : 9:30

ASEC Report ID : 95674
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 06/26/2026 17:00
ASEC Technician Name : Clyde Smith


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date the writer was on site as requested and observed the paving contractor continue subbase preparation with clipping and wetting stone and preparing for proof-rolling. The contractor string lined depth elevations from top of curb and roadway asphalt measuring 8" to 8.5". One small, isolated area at the drive exit lane was observed having slight movement under traffic with recommendation to repair. The contractor has elected to continue compacting efforts for repair.


The writer also met with the paving contractor and grading contractor and Mr. Mcswain to discuss demo and installation of new curbing at the bridge round about.

The writer observed the blasting contractor on site today begin drilling for the pond at Seven Hills Phase 13.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

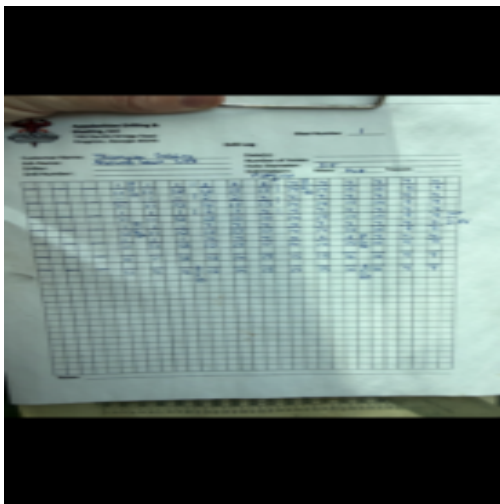

Drilling log for today at pond

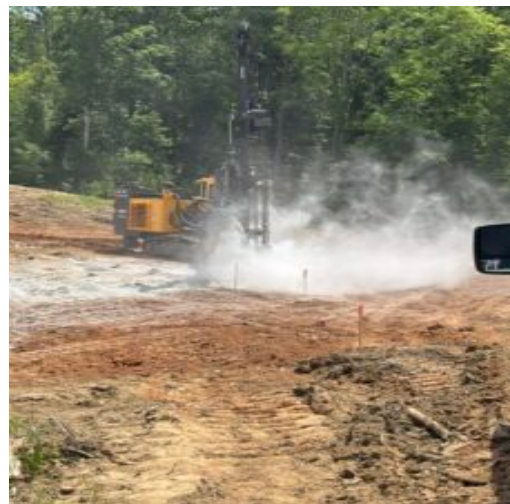

Drilling at pond phase 13

Date : 06/26/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 06/26/2026 07:30
Onsite Hours : 9:30

ASEC Report ID : 95674
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 06/26/2026 17:00
ASEC Technician Name : Clyde Smith



Subbase prep.



String line for depth check

Date : 06/26/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 06/26/2026 07:30
Onsite Hours : 9:30

ASEC Report ID : 95674
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 06/26/2026 17:00
ASEC Technician Name : Clyde Smith



Fine grading subbase



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
