

Date : 07/06/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 07/06/2026 13:00
Onsite Hours : 02:00

ASEC Report ID : 95980
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : sunny
Departure Time : 07/06/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.



At Road C adjacent to Lot 28, the crew excavated the trench to the required depth and leveled the subgrade prior to pipe installation. Two parallel 4-inch PVC sewer service pipes, each approximately 30 feet in length, were installed. At Lots 31 and 34, the crew installed one 4-inch PVC sewer service pipe at each lot. At Road D near Lot 56, one 4-inch PVC sewer service pipe was installed. At Lot 57, two 4-inch PVC sewer service pipes were installed parallel to each other. After installation, backfill material was placed around and above the pipes in lifts and compacted using a trench compactor. The upper portions of the backfill were further compacted using a sheep foot roller.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 07/06/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 07/06/2026 13:00
Onsite Hours : 02:00

ASEC Report ID : 95980
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : sunny
Departure Time : 07/06/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

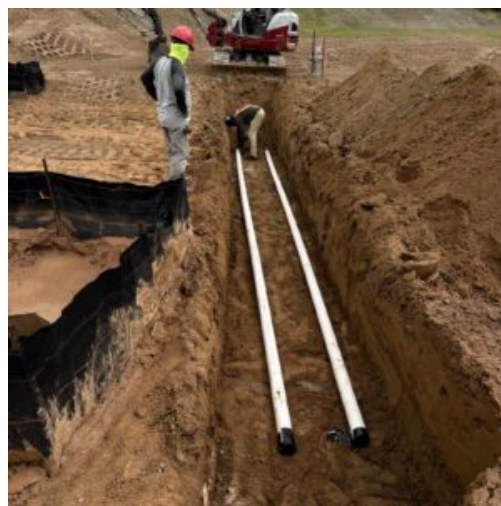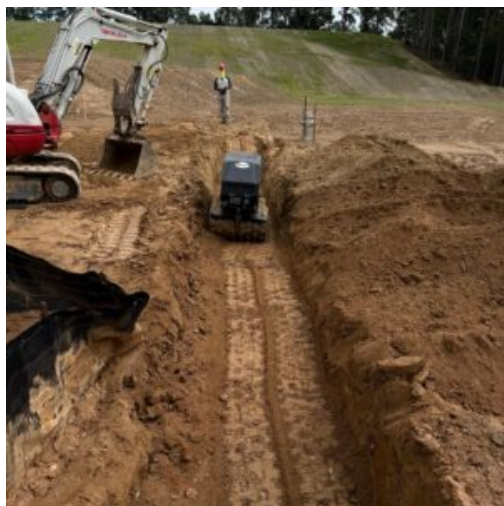

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
