

Date : 06/25/2026
Project No : 2026C136
Client Company : RS Homes
Arrival Time : 06/25/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 95545
Name of the Project : Collett Farms Storm Line & Pavement
Project Location : Canton
Weather : sunny
Departure Time : 06/25/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


For the road area, fill material was delivered and placed by the contractor using an articulated dump truck. The material was spread and graded with a crawler bulldozer. The placed material was then compacted using a sheep-foot roller with multiple passes performed. Field density tests were performed on the compacted fill material. Based on the test results, the compacted fill met the project-required compaction specifications.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 06/25/2026
Project No : 2026C136
Client Company : RS Homes
Arrival Time : 06/25/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 95545
Name of the Project : Collett Farms Storm Line & Pavement
Project Location : Canton
Weather : sunny
Departure Time : 06/25/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

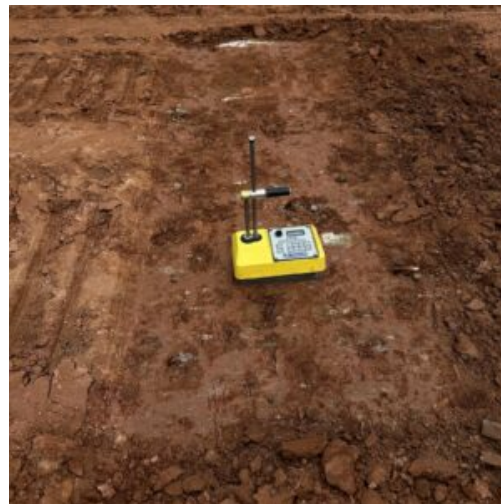

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
