

Date : 07/23/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 07/23/2026 07:30
Onsite Hours : 08:30

ASEC Report ID : 96390
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : Sunny
Departure Time : 07/23/2026 16:00
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was onsite to observe the curb contractor continue pouring type 2 curbing at Seven Hills unit 3 phase 13 roadway. Observation of subgrade soils at the roadway during traffic during pouring curbing indicates the undercutting of rain saturated soils that will require repairs to stabilize.


The writer also met with members from NWGP to discuss discrepancies of previous place asphalt binder mix at unit 4 phase 1A having moderate cracking and segregated areas with low density readings. The contractor acknowledged discrepancies and wanted to re-observe to determine the cause prior to making repair measures.

The writer also observed the pipe contractor installing and backfilling 18" RCP storm lines between structures Y6 to Y6.1 and 2.1 to 3.1. The backfill and compaction efforts appeared to be suitable as per job specifications.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Type 2 curbing poured at Seven Hills unit 3 phase 13 roadway

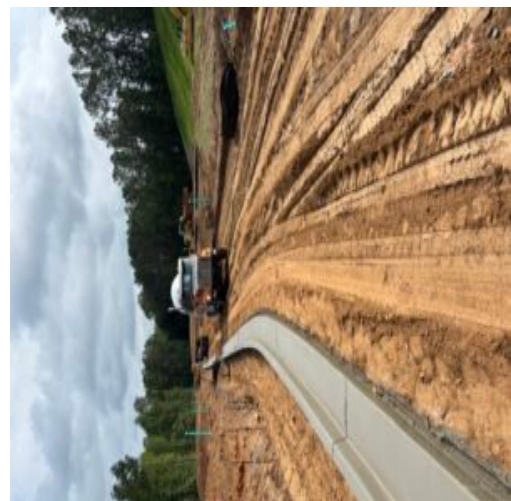

Date : 07/23/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 07/23/2026 07:30
Onsite Hours : 08:30

ASEC Report ID : 96390
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : Sunny
Departure Time : 07/23/2026 16:00
ASEC Technician Name : Clyde Smith



Sub grades observe at unit 3 phase 13 roadway which will require repair




Backfill and compacting efforts at 18" rcp storm lines between Y6 & Y6.1 and 2.1 & 3.1 at unit 4 parkway phase 2



Date : 07/23/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 07/23/2026 07:30
Onsite Hours : 08:30

ASEC Report ID : 96390
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : Sunny
Departure Time : 07/23/2026 16:00
ASEC Technician Name : Clyde Smith

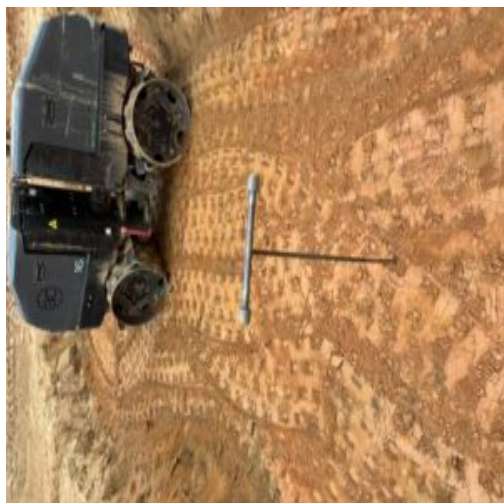

Kenneth Mosman
Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
