

Date : 07/13/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/13/2026 07:30
Onsite Hours : 06:00

ASEC Report ID : 96204
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : cloudy
Departure Time : 07/13/2026 13:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was onsite to meet with the paving contractor (NWGP) and to observe subgrade and subbase conditions after a recent rain event. The remaining subgrade soils approximately 150' both sides of roadway appeared too wet with rutting observed from subcontractor traffic. With additional rain forecasted for today it was decided not to repair and place additional base stone today. The paving contractor remained onsite setting grade stakes and blading the roadway.

Our representative observed the grading contractor backfilling poured curbing at the roundabout.

The writer also observed the wall contractor installing reinforcing steel for the bridge panels.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.





Observation of reinforcing steel being installed at bridge panels



Date : 07/13/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/13/2026 07:30
Onsite Hours : 06:00

ASEC Report ID : 96204
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : cloudy
Departure Time : 07/13/2026 13:30
ASEC Technician Name : Clyde Smith

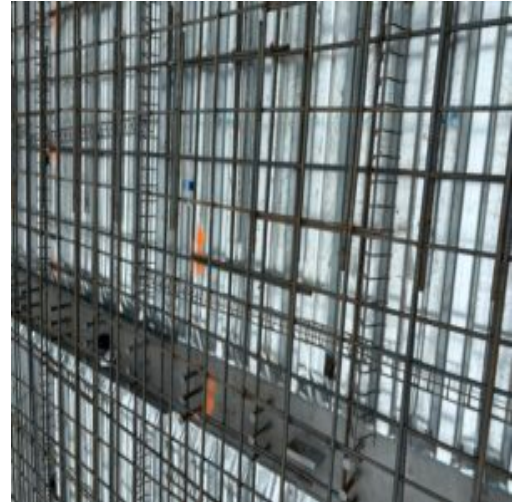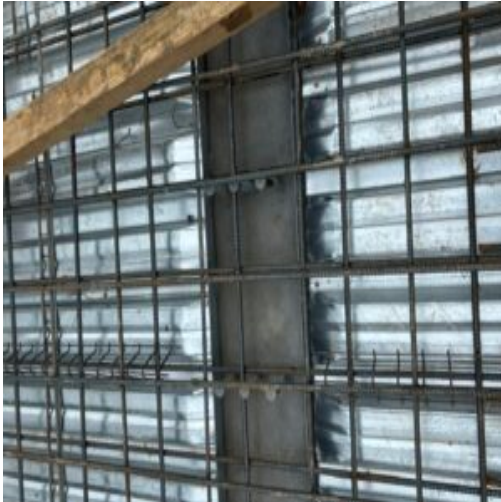


Backfill at round about curbing




Paving contractor installing grade stakes at
Nature Walk

Date : 07/13/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 07/13/2026 07:30
Onsite Hours : 06:00

ASEC Report ID : 96204
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : cloudy
Departure Time : 07/13/2026 13:30
ASEC Technician Name : Clyde Smith

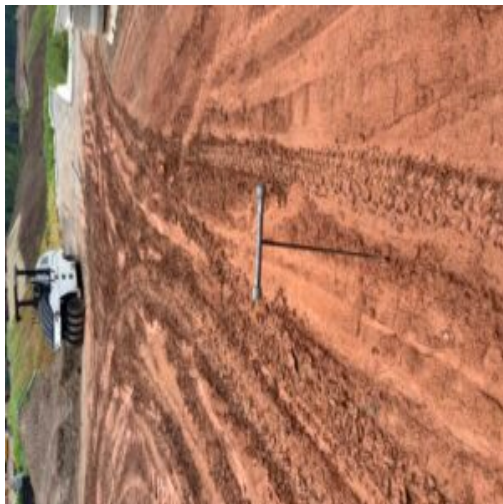

Observation of sub grade after rain event at Nature Walk

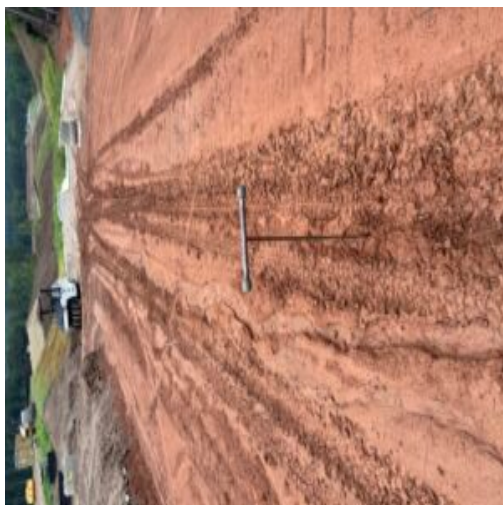

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
