

Date : 06/29/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 06/29/2026 07:30
Onsite Hours : 9:00


ASEC Report ID : 95796
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 06/29/2026 16:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the paving contractor perform subbase preparation for the deceleration lane at Seven Hills Boulevard and the drive roadway to building lots using a loaded tandem dump truck having over 18 tons. Proof-rolling was performed for the in place subbase stone. The proof-roll was also observed with other members from Paulding County, J & W Paving and Thompson Grading. The subbase appeared stable under traffic except one small, isolated area (12' x 20') located at the exit drive having utility lines in place. Recommendation made was to clip repair the area -2" and replace with additional 25mm asphalt base mix. The subbase proof-roll and repair recommendation was accepted by the county official with approval for asphalt paving.

The writer also observed the blasting contractor continue drilling rock for the on-site detention pond. See attached drill log.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

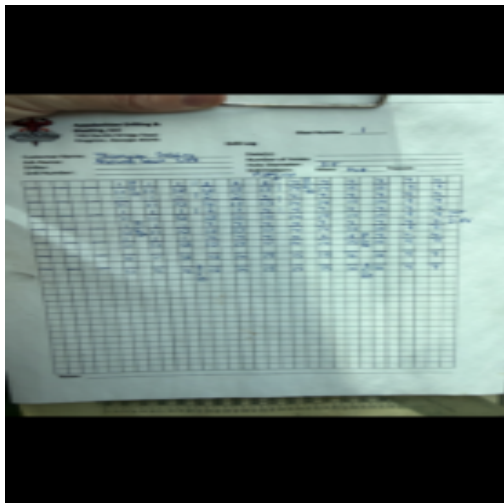

Drill and blast log for first blast at detention pond




Drilling site location

Date : 06/29/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 06/29/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 95796
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 06/29/2026 16:30
ASEC Technician Name : Clyde Smith



Sub base proof roll at decel. lane and roadway being observed by Paulding County, J&W Paving and Thompson Grading

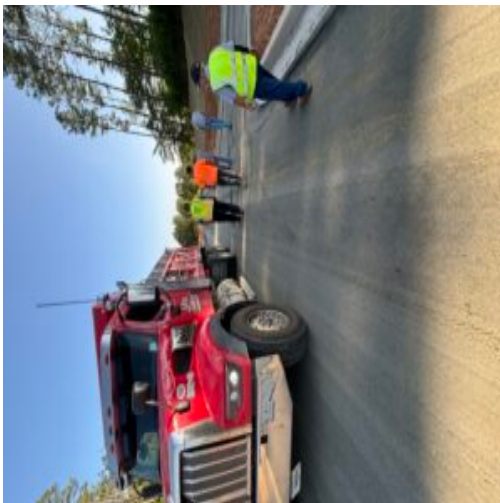

Date : 06/29/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 06/29/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 95796
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 06/29/2026 16:30
ASEC Technician Name : Clyde Smith



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
