

Date : 07/02/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 07/02/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 95855
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 07/02/2026 16:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


On the above date our representative was on site to observe the paving contractor (JW) continue asphalt paving placing topping mix (12.5) for the deceleration lane and entrance radius drive. The contractor placed approximately 55 tons of topping mix. Temperature checks were performed on truck loads. Compacting equipment appeared to be adequate for placement.

The writer also observed the grading contractor (Thompson) continue fill placement at the roadway over the Plantation gas line. The fill was compacted using a sheet-foot roller in the static mode. The fill was probed using a rounded end steel rod and also observed under the traffic of an off-road dump truck which indicated no movement. This observation is suitable for compaction requirements.


The blasting contractor made the second rock blast for the detention pond.

The writer observed the curbing contractor pouring type seven curbing at the east side bridge roundabout.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

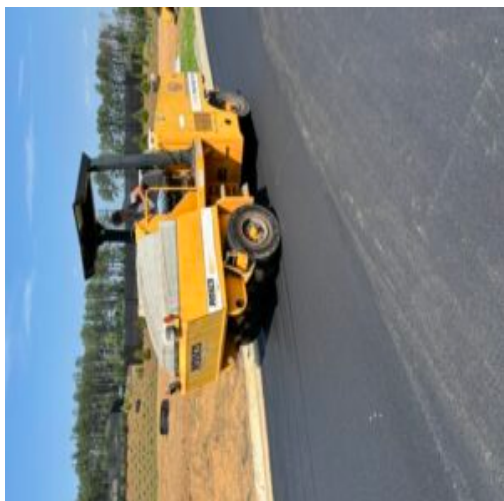


Asphalt paving placement (12.5) mix at deceleration lane

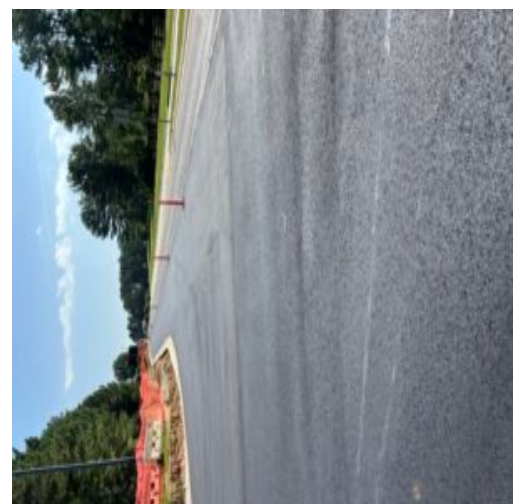

Date : 07/02/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 07/02/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 95855
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 07/02/2026 16:30
ASEC Technician Name : Clyde Smith

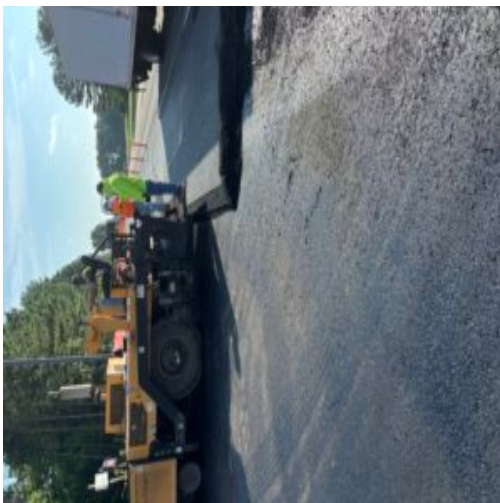

Asphalt batch ticket

Date : 07/02/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 07/02/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 95855
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 07/02/2026 16:30
ASEC Technician Name : Clyde Smith



Fill placement and compacting efforts at roadway over gas line.



Drill blast log

Date : 07/02/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 07/02/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 95855
Name of the Project : Seven Hills PHASE 13, UNIT 4 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 07/02/2026 16:30
ASEC Technician Name : Clyde Smith



Curbing pour at round about



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
