

Date : 07/17/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 07/17/2026 08:00
Onsite Hours : 10:30

ASEC Report ID : 96296
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : cloudy
Departure Time : 07/17/2026 18:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was onsite to observe and assist in testing concrete placement for the dead man footing for the east side wall. One set of (6) 4 x 8 test cylinders were made for the 50 cubic yards poured.

Continued observation of reinforcing steel being installed for the bridge slab panels. Recommendations made were to move vertical bars off top of nelson stubs in panels for sufficient clearance. Contractor also completed clean-up of trash and debris off panels. The writer observed added #6 bars (vertical) under the support plate holding threaded dowel bolts for hanging the sanitary sewer line under the bridge.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Monitoring concrete pour and testing at dead man footing wall



Date : 07/17/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 07/17/2026 08:00
Onsite Hours : 10:30


ASEC Report ID : 96296
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : cloudy
Departure Time : 07/17/2026 18:30
ASEC Technician Name : Clyde Smith



Observation of reinforcing steel in place at bridge slab panels according to site document in title Bridge Deck,dated 2/20/26.Drawing No. R3.0



Vertical #6 bars added at support bolts for hanging sanitary sewer line

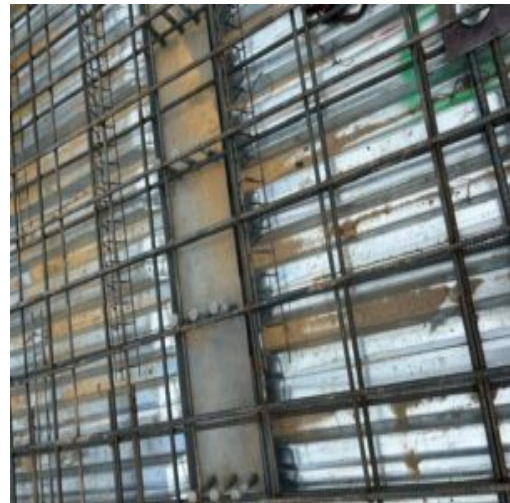

Date : 07/17/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 07/17/2026 08:00
Onsite Hours : 10:30

ASEC Report ID : 96296
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : cloudy
Departure Time : 07/17/2026 18:30
ASEC Technician Name : Clyde Smith



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
