


Date : 06/29/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 06/29/2026 12:00
Onsite Hours : 02:00

ASEC Report ID : 95706
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : sunny
Departure Time : 06/29/2026 14:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The crew continued installing the water line along Road C. The area was excavated to the required depth, the subgrade was leveled, and approximately 120 lineal feet of 8-inch DIP was installed in the northeast direction. After installation, backfill material was placed and compacted using a trench compactor and sheep-foot roller.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

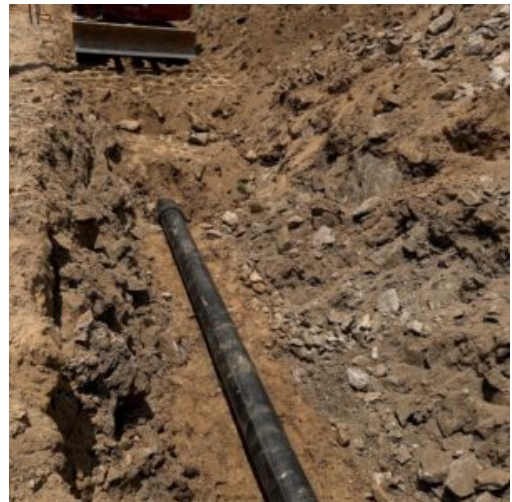

Date : 06/29/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 06/29/2026 12:00
Onsite Hours : 02:00

ASEC Report ID : 95706
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : sunny
Departure Time : 06/29/2026 14:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
