

Date : 08/04/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 08/04/2026 07:30
Onsite Hours : 04:00

ASEC Report ID : 96649
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : cloudy
Departure Time : 08/04/2026 11:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


On the above date our representative was onsite to observe the grading contractor Thompson continue placing fill for Lots #33 and 34.

The pipe contractor Savannah was also onsite to begin installing 8" DIP sanitary sewer line crossing the colonial gas pipeline at phase 13 between C 13 and C 14 manhole structures. The grading contractor Thompson also continued hammering rock and excavating at the phase 13 detention pond.

The curb contractor J & W begin installing 30" curbing at Naturewalk Parkway phase 1 between sanitary sewer manholes #14 and 13 pouring a 3000 mix.

The writer observed the grading contractor Thompson begin hauling fill to the bridge abutment wall with backfill being placed and compacted by the wall contractor RWS covering tension cables between the abutment wall and the dead man footing wall. The contractor placed approximately one lift of compacted fill prior to an afternoon rain event that stopped fill placement.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.


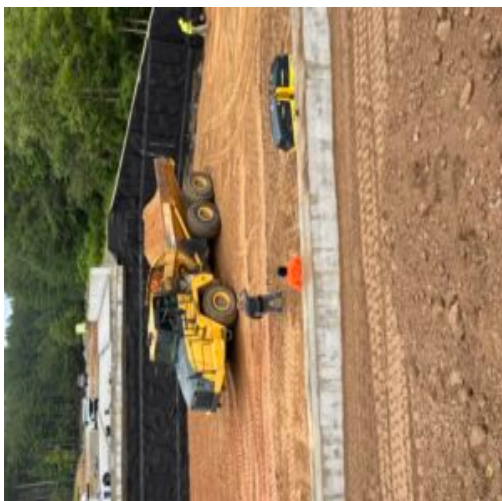


Fill placement between abutment wall and dead man wall





Date : 08/04/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 08/04/2026 07:30
Onsite Hours : 04:00

ASEC Report ID : 96649
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : cloudy
Departure Time : 08/04/2026 11:30
ASEC Technician Name : Clyde Smith

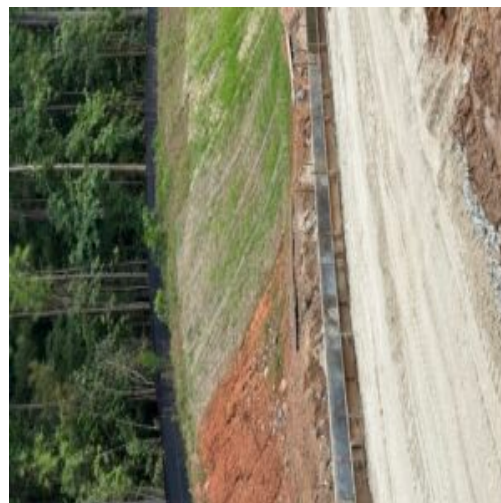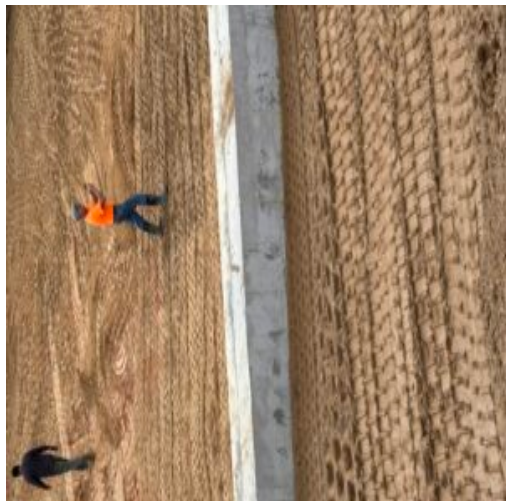

Poured curbing at Nature Walk Pkwy. between
sanitary sewer manhole # 14 and 13

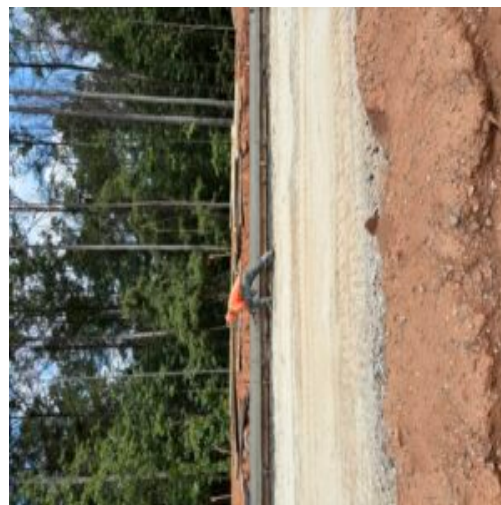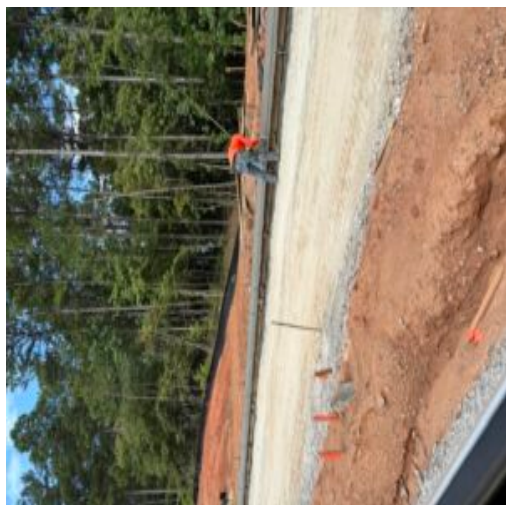

Date : 08/04/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 08/04/2026 07:30
Onsite Hours : 04:00

ASEC Report ID : 96649
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : cloudy
Departure Time : 08/04/2026 11:30
ASEC Technician Name : Clyde Smith



Backfill over tension rods between abutment wall
and dead man footing wall



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
