

Date : 08/11/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 08/11/2026 12::3
Onsite Hours : -7:00

ASEC Report ID : 96770
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAIA, Atlanta, GA
Weather : clear and sunny
Departure Time : 08/11/2026 5:00
ASEC Technician Name : Narayana Ganesh Undavalli

On the above date, an AS Engineering and Consulting, LLC (ASEC) representative visited the site at the contractor's request to **observe excavation and subgrade preparation activities** associated with the airfield repair work at **Taxiway Golf**, specifically along the **slope on the north side of Taxiway Golf**, in accordance with the project drawings and specifications.

Prior to excavation, the contractor **marked the limits of the proposed work area**. The contractor then performed grading and excavation to an approximate depth of **36 inches** for construction of the proposed **concrete drainage structure and associated drain pipe** along the north slope of Taxiway Golf.

Excavated soil was removed from the work area using a **tandem-axle dump truck**. Following excavation, the exposed subgrade was leveled and compacted using a **trench compactor** in preparation for subsequent construction activities.

No density testing was reported as being performed by ASEC during these activities on this date.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



slop area



concrete structure

Date : 08/11/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 08/11/2026 12::3
Onsite Hours : -7:00


ASEC Report ID : 96770
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAIA, Atlanta, GA
Weather : clear and sunny
Departure Time : 08/11/2026 5:00
ASEC Technician Name : Narayana Ganesh Undavalli



Marked area to excavate



Excavating Area

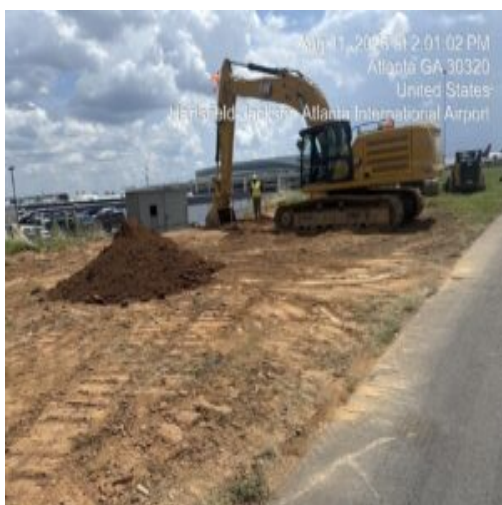

soil extracted from the marked area



compacting excavated area using trench packer.

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
