

Date : 08/12/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 08/12/2026 07:30
Onsite Hours : 08:30

ASEC Report ID : 96864
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : Sunny
Departure Time : 08/12/2026 16:00
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the curbing contractor continue installing 30" curb at Naturewalk Parkway. The contractor installed approximately 300 lineal feet of curbing using a 3000-psi concrete mix.

The grading contractor continued hammering rock at Unit 4 phase 2.

The grading contractor also began placing fill at the recently cleared area for Unit 4 Phase 3, specifically, Lots #95, 96 and 97 in compacted lifts.

Fill placement at the bridge abutment was cancelled today due to saturated in-place soils from a recent rain event.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Pouring 30" curbing at Nature Walk Pkwy




Date : 08/12/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 08/12/2026 07:30
Onsite Hours : 08:30

ASEC Report ID : 96864
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : Sunny
Departure Time : 08/12/2026 16:00
ASEC Technician Name : Clyde Smith



Placing fill at Unit 4 phase 3 lots 95,96 and 97.

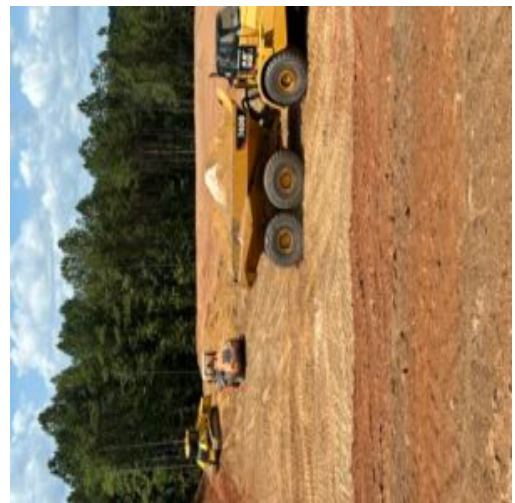

Date : 08/12/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 08/12/2026 07:30
Onsite Hours : 08:30

ASEC Report ID : 96864
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : Sunny
Departure Time : 08/12/2026 16:00
ASEC Technician Name : Clyde Smith



Installation of 30" curbing



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
