

Date : 08/20/2026
Project No : 2026C119
Client Company : SR Homes
Arrival Time : 08/20/2026 8:00
Onsite Hours : 9:00

ASEC Report ID : 97019
Name of the Project : Township @ Jennings Mill - Classic Rd
Project Location : Athens
Weather : clear and sunny
Departure Time : 08/20/2026 17:00
ASEC Technician Name : Narayana Ganesh Undavalli



As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The crew excavated the soil to a depth of approximately 4 feet below existing ground level to a length of approximately 300 feet around the pond in order to build a keyway. Our representative visually checked the excavated area using a 3/8" diameter probe rod to verify stability to start back fill around the pond for the keyway.

The crew started placing gill material in lifts, spread using a crawler bulldozer, and compacted using vibratory roller (SV 540T) Density tests were performed, and the results met the required project compaction specifications.


On the other side of the site the crew continued in clearing vegetation.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

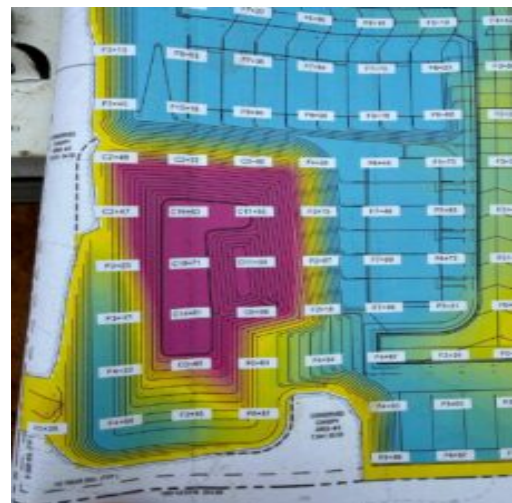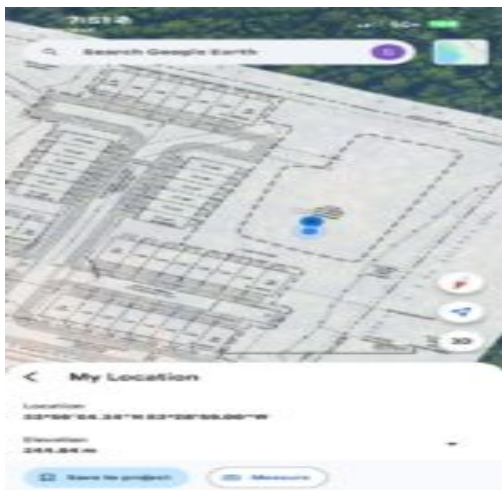

Date : 08/20/2026
Project No : 2026C119
Client Company : SR Homes
Arrival Time : 08/20/2026 8:00
Onsite Hours : 9:00

ASEC Report ID : 97019
Name of the Project : Township @ Jennings Mill - Classic Rd
Project Location : Athens
Weather : clear and sunny
Departure Time : 08/20/2026 17:00
ASEC Technician Name : Narayana Ganesh Undavalli

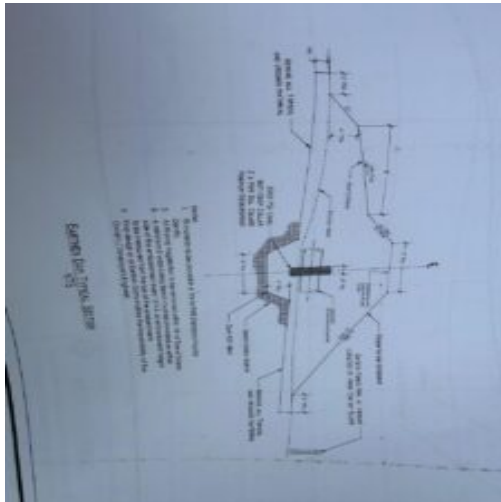

Date : 08/20/2026
Project No : 2026C119
Client Company : SR Homes
Arrival Time : 08/20/2026 8:00
Onsite Hours : 9:00

ASEC Report ID : 97019
Name of the Project : Township @ Jennings Mill - Classic Rd
Project Location : Athens
Weather : clear and sunny
Departure Time : 08/20/2026 17:00
ASEC Technician Name : Narayana Ganesh Undavalli



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
