

Date : 09/16/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/16/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97686
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/16/2026 17:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the grading contractor continue excavation at the borrow pit and placing fill at building Lots #13 thru 15 using clean soil fill. The contractor also placed rockfill at the old temporary detention pond in roadway near sanitary sewer manhole Z19. Density tests were performed at building Lots #10 thru 14 using a Troxler Nuclear gauge model 3430, serial no. 91643. Compaction results were suitable as per job specifications. The rockfill placement at the old detention pond was in compliance with recommendations and suitable for compaction requirements. The contractor also began filling the excavated borrow pit with broken boulders.


The pipe contractor raised manholes Z19 and Z19.1.

The writer also observed existing stockpiled materials at south side at Shelly Boulevard by dug test pits to determine suitability for structure fill placement at building lots. The fill contained some boulders, topsoil and saturated soils. The materials were recommended for placement at the slope embankments. The material will be monitored during excavation to determine suitability for structure fill suitability.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.




Test pits observed at onsite stockpile at Shelly Blvd.


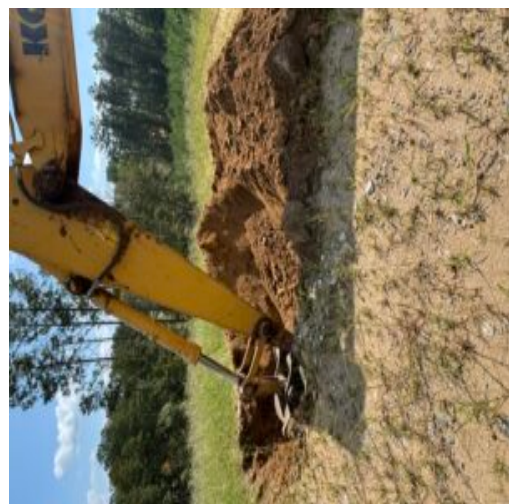


Date : 09/16/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/16/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97686
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/16/2026 17:30
ASEC Technician Name : Clyde Smith

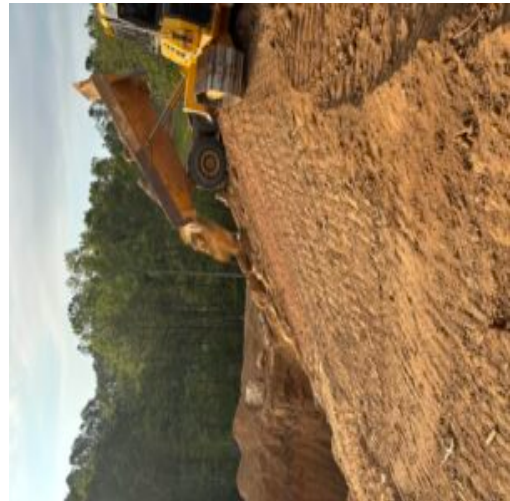


Excavation at borrow pit and rock fill replacement

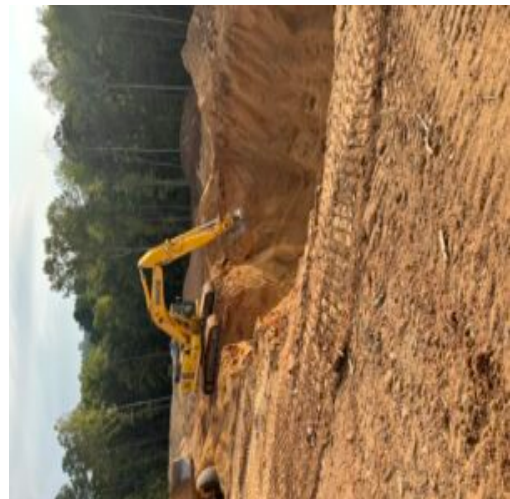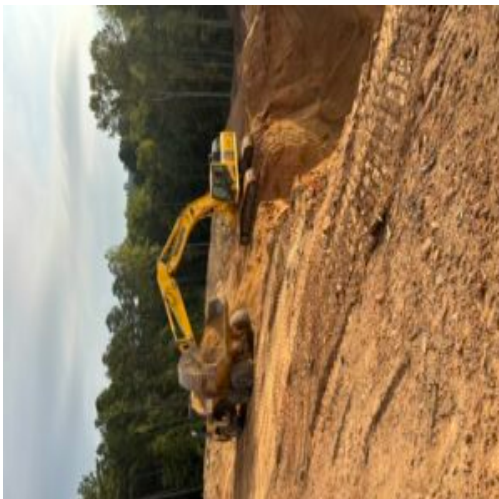


Date : 09/16/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/16/2026 07:30
Onsite Hours : 10:00


ASEC Report ID : 97686
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/16/2026 17:30
ASEC Technician Name : Clyde Smith

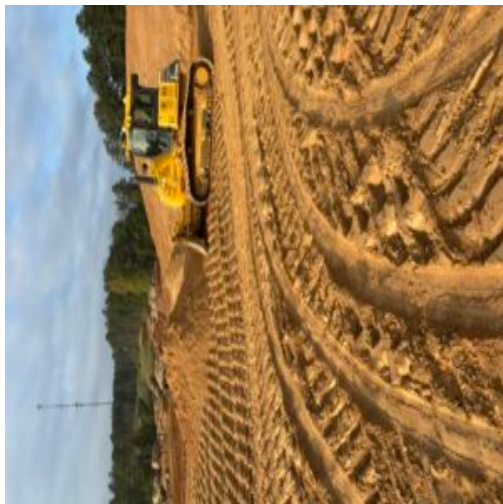

Fill placement at building lots

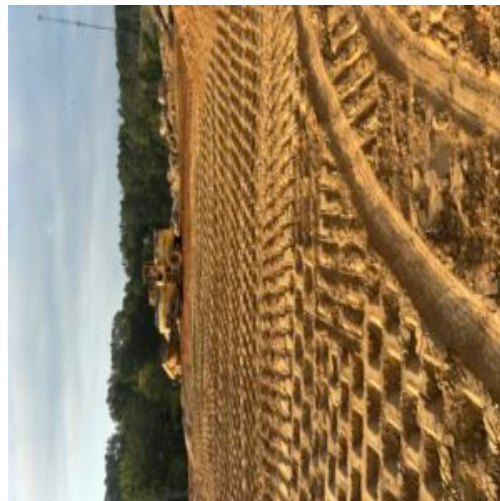


Placing boulder fill at excavated borrow pit

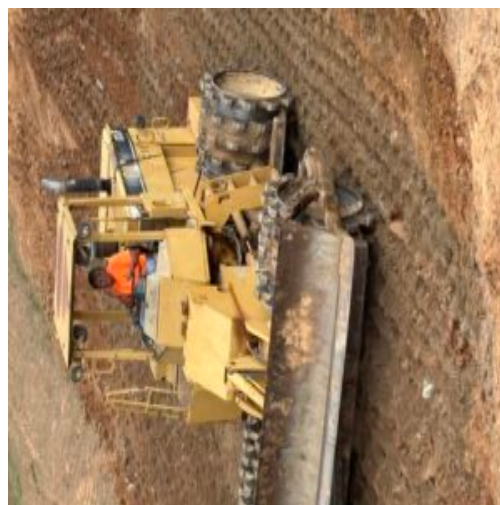


Compacting rockfill and placement at old detention pond in roadway near Z19

Date : 09/16/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/16/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97686
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/16/2026 17:30
ASEC Technician Name : Clyde Smith

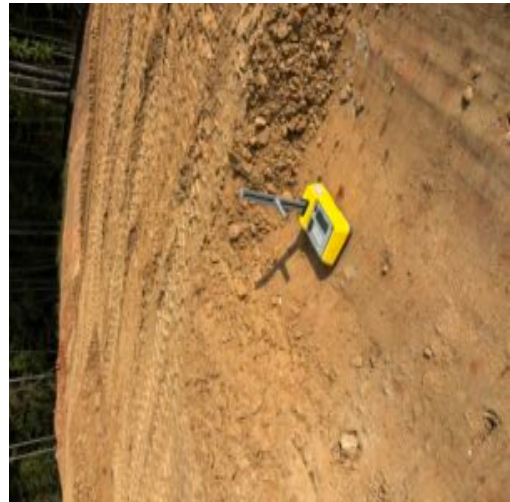

Density tests performed at building lots 10 thru 14

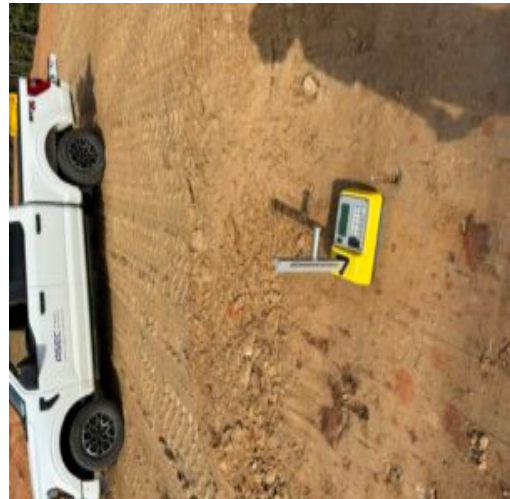

Date : 09/16/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/16/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97686
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/16/2026 17:30
ASEC Technician Name : Clyde Smith



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
