

Date : 09/21/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/21/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97787
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/21/2026 17:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the grading contractor Thompson continue placing fill for the roadway between sanitary sewer manholes Z 18 and Z 20. Also placed fill for building Lots #10 thru 15. Density tests were performed using a Troxler Nuclear gauge model 3430, serial no. 91643.

The writer observed the pipe contractor Savannah backfilling 18" RCP storm line between manhole #B6 and B8.


The wall contractor RWS had concrete cores cut at the east and west sides of the bridge for electrical conduits installation. The contractor cut 12 six-inch cores that were twelve inches in length.

The writer also met with the grading and paving contractors to discuss subgrade preparation at the east side of bridge on NatureWalk Parkway.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.






6" core holes cut at bridge for electrical conduits installation

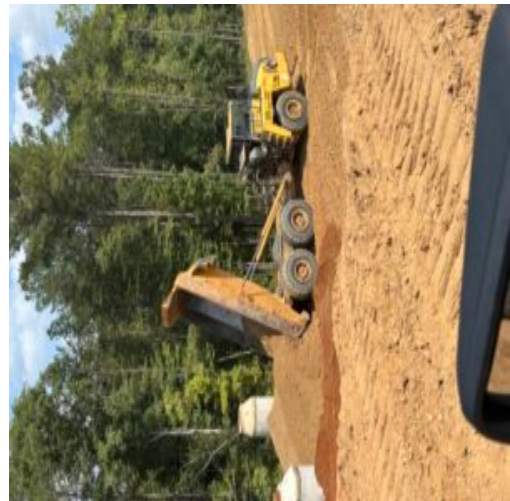

Placing fill at roadway between S.S. manholes # Z18 and Z 20

Date : 09/21/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/21/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97787
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/21/2026 17:30
ASEC Technician Name : Clyde Smith

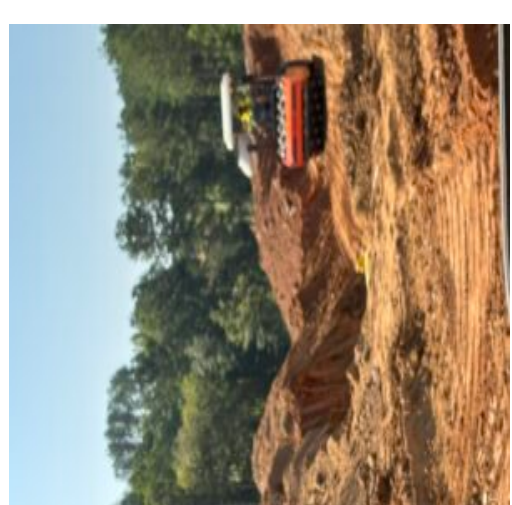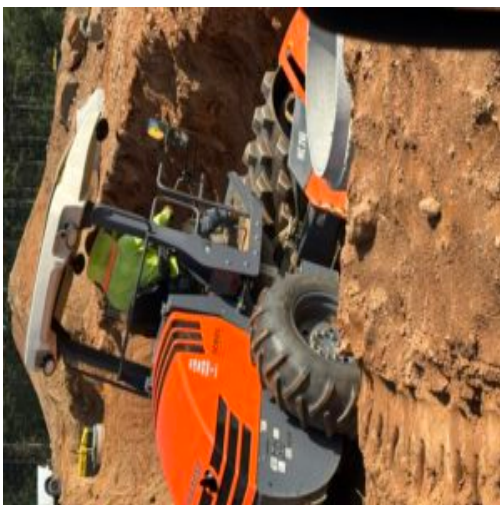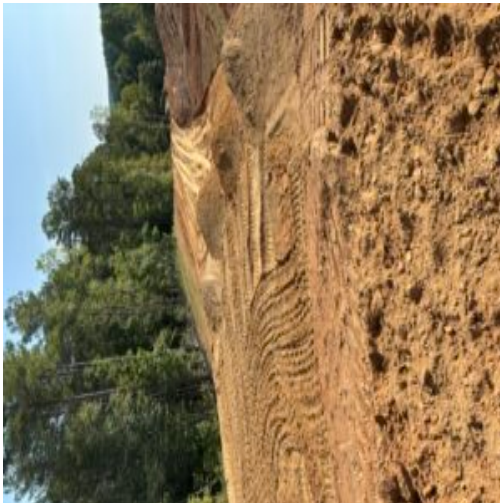

Backfill at 18" rcp storm between B 6 and B 8



AS Engineering
and Consulting LLC

Daily Field Report

Date : 09/21/2026
Project No : 2026C101
Client Company : Artisan
Arrival Time : 09/21/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97787
Name of the Project : Seven Hills PHASE 13, UNIT 3 Lots
Project Location : Dallas
Weather : Sunny
Departure Time : 09/21/2026 17:30
ASEC Technician Name : Clyde Smith

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
