

Date : 09/23/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 09/23/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97823
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : Sunny
Departure Time : 09/23/2026 17:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative observes the grading contractor Thompson placing fill at Unit 4 phase 3 building lots. There was no additional information available for lot numbers or elevations, however, the approximate depth is 8 feet below finished grade. The writer performed density tests using a Troxler Nuclear gauge model 3430, serial no. 91643. Compaction results were suitable for requirements of 95 % to 98 %.

The writer also observed the paving contractor continue subgrade preparation at Nature Walk Parkway between sanitary sewer manhole #3 and #2. The subgrade was proof-rolled using a loaded tandem dump truck. The subgrade soils appeared stable under traffic except one small, isolated area (12' x 6') which was clipped -4" and replaced with additional base stone. The contractor plans to start placing base stone tomorrow.


The grading contractor Thompson backfilled the electrical conduit holes at the east and west side bridge abutments. Compaction results met project specifications.

The grading contractor also continued fill placement at Seven Hills Unit 4 phase 13 building Lots #22 and 23. Fill soils with some rock fragments were used in filling in borrow pit #2 south of building Lot #24.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.






Fill soils being placed back into excavated borrow pit #2 south of building lot # 24

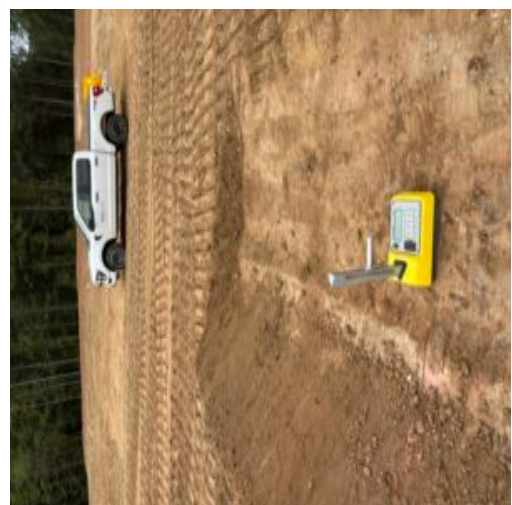

Density tests performed at Unit 4 phase 3

Date : 09/23/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 09/23/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97823
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : Sunny
Departure Time : 09/23/2026 17:30
ASEC Technician Name : Clyde Smith

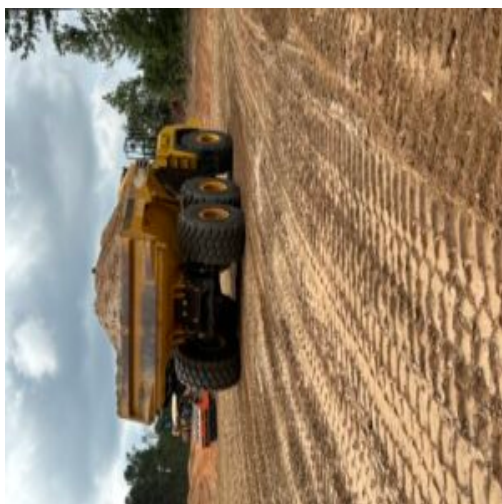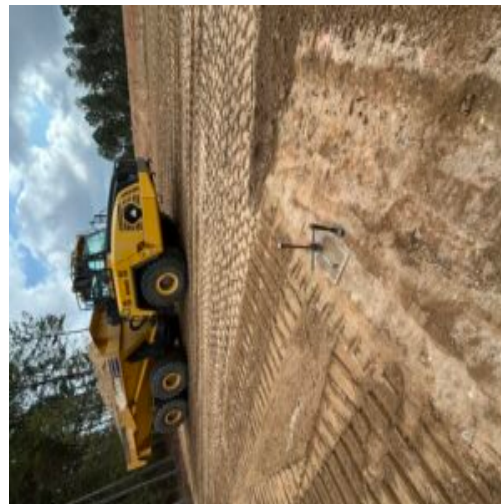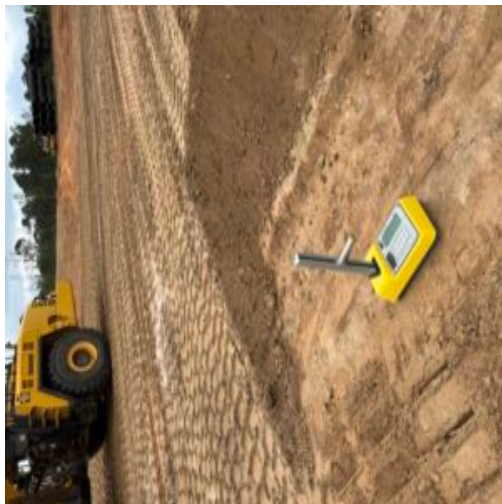

Additional Compacting efforts recommended using off road dump truck.


Backfilling at electrical conduits holes at bridge abutments.

Date : 09/23/2026
Project No : 2026C103
Client Company : Artisan
Arrival Time : 09/23/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97823
Name of the Project : NW PH 2, UNIT 4
Project Location : Dallas
Weather : Sunny
Departure Time : 09/23/2026 17:30
ASEC Technician Name : Clyde Smith



Observing proof rolling of subgrade at Nature Walk Pkwy. between sanitary sewer manhole #3 and #2

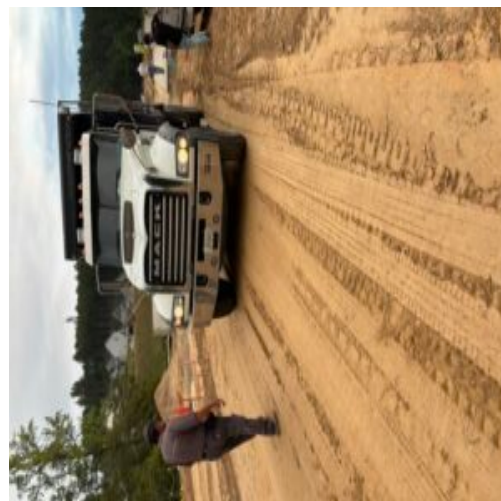

Truck ticket used for proof roll

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
