

Date : 10/21/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/21/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98245
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/21/2026 16:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


On the above date our representative observed the grading contractor Thompson demo asphalt for the roundabout. The contractor hauled off demo asphalt and also begin hauling off demo concrete and trash debris stockpiled at the building lot. The contractor also continued drying excavated stockpiled washed silt materials from the detention pond at Unit 4, Phase 2. These materials are planned for placement at the slope embankment rear of the amenity parking lot.

The curb contractor J&W was onsite and began forming for the outer and inner curb pour at the roundabout and also meeting with County officials continuing to discuss installation and requirements for poured curbing. The writer observed existing subbase materials after removal of demo asphalt and approved in place materials to be suitable consisting of compacted subbase stone and other areas having soil cement in place. Typical details received from the county showed a minimum of 4" compacted subgrade in place. Existing materials in place was approved for the placement of curbing.

The drilling contractor also continued drilling hard rock at Unit 4, Phase 3 planning to blast on 10/23/2026.

The writer met with the client, the grading contractor and the bush hog contractor to discuss clearing for access roads entrances for under bridge repairs.


We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

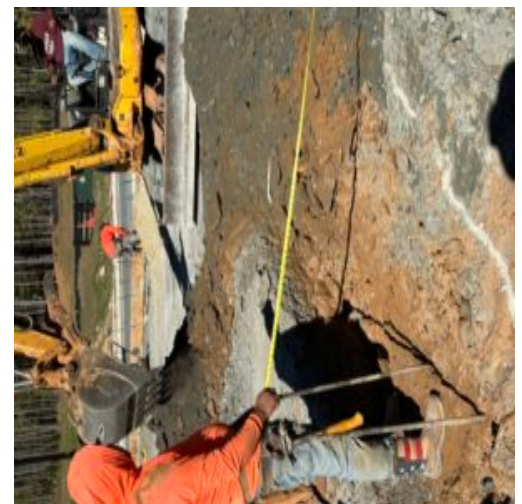


Subbase prep.and forming for outer and inner curb pours.

Date : 10/21/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/21/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98245
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/21/2026 16:30
ASEC Technician Name : Clyde Smith

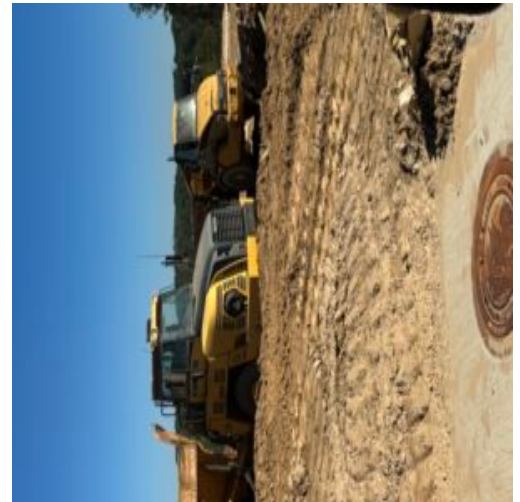

Drying and moving stockpiled materials

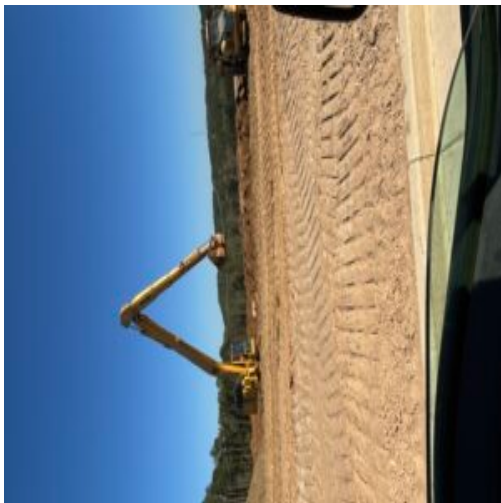


Forming for curbing

Date : 10/21/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/21/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98245
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/21/2026 16:30
ASEC Technician Name : Clyde Smith



Subgrade prep.at Unit 4 phase 2 roadway

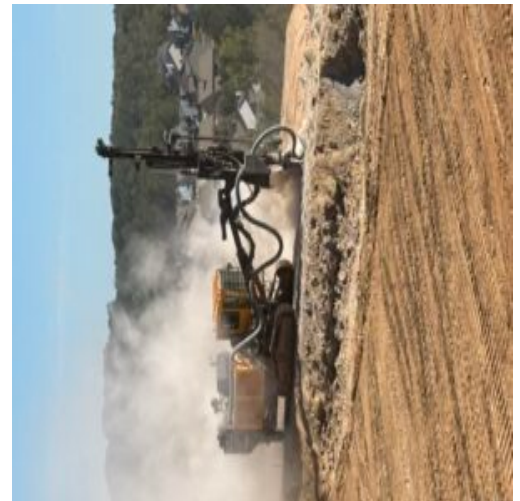

Drilling hard rock at Unit 4 phase 3

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
