

Date : 10/14/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/14/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98106
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/14/2026 16:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


On the above date our representative observed the paving contractor NWGP continue subgrade preparation at the roundabout clipping subgrade soils and stabling at the westside drive to the bridge using Tensar stablization fabric in one isolated area twenty feet long in areas already clipped 4". The contractor completed subgrade preparation, and it was approved for the placement of subbase stone. The contractor continued subbase preparation at the roundabout and also subbase preparation at Nature Walk Parway, west side of bridge, by wetting and compacting.

The grading contractor Thompson begin demucking wash silt from detention pond at Unit 4, Phase 2. The excavated silt materials were removed using a long reach backhoe and was spread along the existing slope at the back of amenity parking lot.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Washed silt in detention pond at Unit 4 phase 2

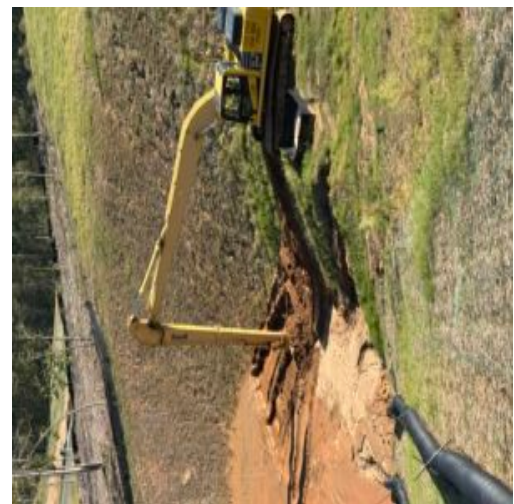

Using the long reach excavator removing washed silt from pond.

Date : 10/14/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/14/2026 07:30
Onsite Hours : 9:00


ASEC Report ID : 98106
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/14/2026 16:30
ASEC Technician Name : Clyde Smith



Subbase prep. at west side of bridge



Compacting subbase at Nature Walk Pkwy.

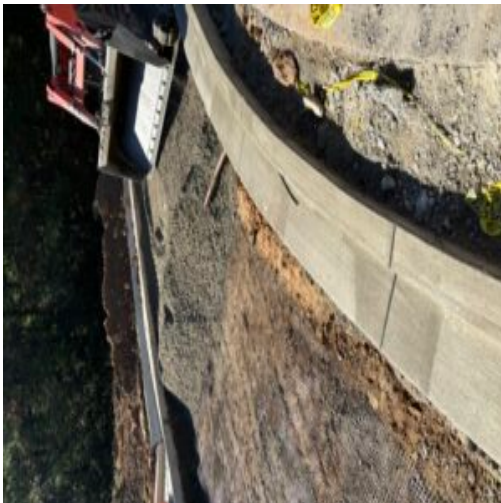

Spreading subbase stone over Tensar fabric at roundabout



Tensar fabric in place

Date : 10/14/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/14/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98106
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/14/2026 16:30
ASEC Technician Name : Clyde Smith




Observing subgrade depth at roundabout



Observing proof roll of subgrade at roundabout




Delivery ticket used for proof roll

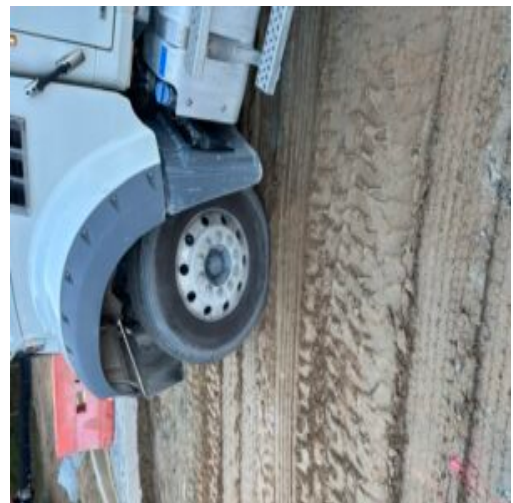

Subgrade proof roll at roundabout

Date : 10/14/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/14/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98106
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/14/2026 16:30
ASEC Technician Name : Clyde Smith

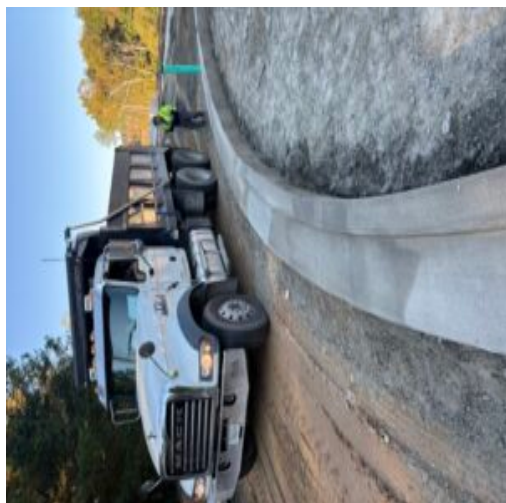

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
