


Date : 10/16/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/16/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98132
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/16/2026 16:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative observed the paving contractor NWGP complete subbase preparation at the east side of the bridge to the roundabout. The writer also observed proof-rolling of the subbase at Nature Walk Parkway on both sides of the bridge using a loaded tandem dump truck loaded with 17.95 tons. The subbase proof-roll appeared stable with no apparent movement under traffic and was approved for asphalt paving. The proof-roll was also observed by other members from Paulding County and NWGP who accepted the results.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

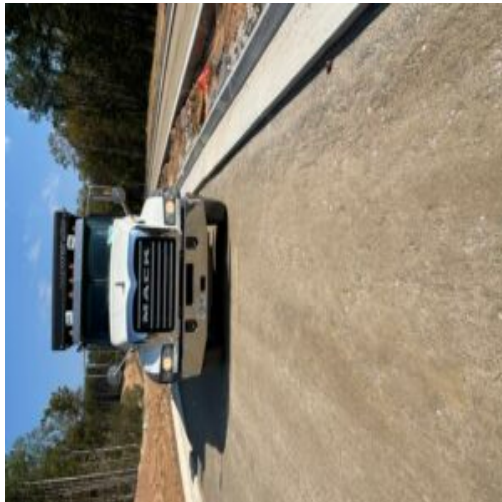

Proof rolling of subbase using a loaded tandem dump truck having 17.95 tons at both sides of bridge.



Date : 10/16/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/16/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98132
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/16/2026 16:30
ASEC Technician Name : Clyde Smith



Date : 10/16/2026
Project No : 2025C215
Client Company : Artisan
Arrival Time : 10/16/2026 07:30
Onsite Hours : 9:00

ASEC Report ID : 98132
Name of the Project : NW Unit 4 Parkway Ext. Phase 1
Project Location : Dallas
Weather : Sunny
Departure Time : 10/16/2026 16:30
ASEC Technician Name : Clyde Smith



Delivery ticket having 17.95 tons

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
