

Date : 03/21/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/21/2023 06:00
Onsite Hours : 10:30



ASEC Report ID : 57978
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather :
Departure Time : 03/21/2023 16:30
ASEC Technician Name : Vidal Dias

Our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Vidal Dias visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to observe, verify and document the ongoing project activities. (Reference drawing E720661 S1 - R5 & E720659 S1-R5.)

During the visit, the following observations were made:

1. Four hundred eighty-six (486) cubic yards of fill material were placed and compacted for the bridge lift in the basement in accordance with ITP-001.
2. The area was probed using a 3/8" diameter probe rod during the placement and the probe did not exceed 1.5 inches into the soil.
3. Seventy-eight point seven-six (78.76) tons of rip-rap was received.
4. The contractor rolled the gravel road and placed additional rip-rap in area H6 (drawing E720659).
5. In area F7, the contractor used a concrete saw to cut a two-inch space on the top edge of the concrete on the north and south side of the trench crossing the road. Two steel one-inch steel plates were placed on the drainage trench.

Photo documentation and test locations are attached:

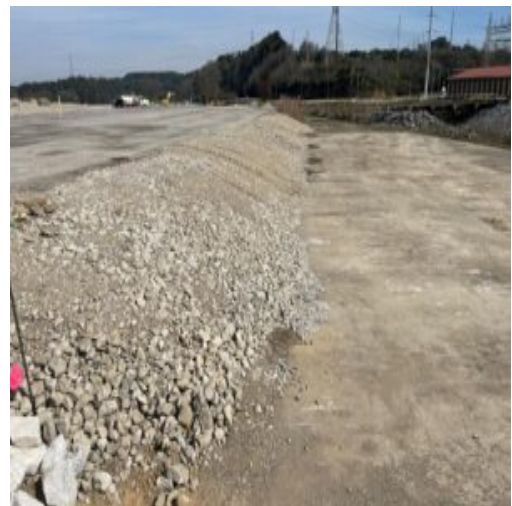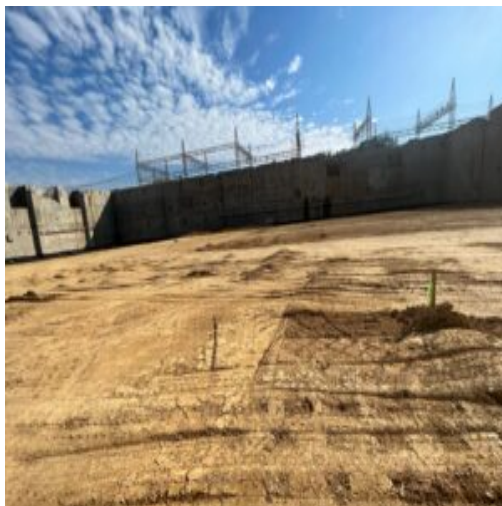

Date : 03/21/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/21/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 57978
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather :
Departure Time : 03/21/2023 16:30
ASEC Technician Name : Vidal Dias



Vidal Dias
070321636
Project Geologist



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
