


Date : 05/04/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 05/04/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59040
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 05/04/2023 16:30
ASEC Technician Name : Avinash Bandham

Our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to observe, verify and document the ongoing project activities. (Reference drawing E720661 S1 - R5, E720659 S1-R5.)

During the visit, the following observations were made:

1. Two thousand three hundred and fifty-eight (2358) cubic yards of fill materials were placed for lift (10) in section 1 area B7 (drawing E720661) of the basement. The materials were placed and compacted in accordance with ITP-001. The blue highlighted area in the drawing E720661 shows the placement of the fill material in the section 1.
2. The edges of the north, east, west and south walls of the section 2 in basement was probed using a 3/8" diameter probe rod as requested by client Mr. Terry Polena representative of Jacksonville Demolition.

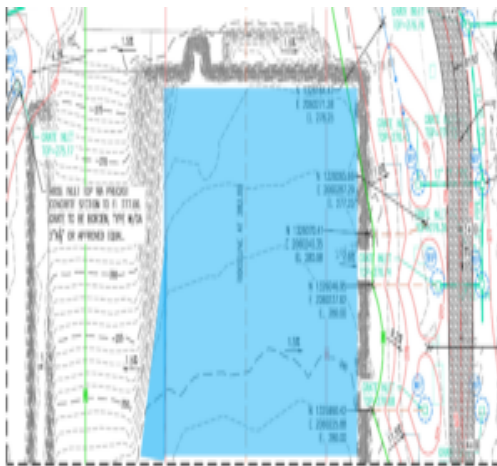

Placement of Lift-10 in the section-1 basement area B7.



Compaction using the roller and dozer.

Date : 05/04/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 05/04/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59040
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 05/04/2023 16:30
ASEC Technician Name : Avinash Bandham



Loads received and delivered to the site for the placement in section-1.



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
