



Date : 05/12/2026
Project No : 2025C187
Client Company : CWM
Arrival Time : 05/12/2026 10:00
Onsite Hours : 05:00

ASEC Report ID : 94331
Name of the Project : Lee Gilmer Memorial Airport - Rehab
Terminal Area Apron PH 3
Project Location : Gainesville
Weather : Sunny
Departure Time : 05/12/2026 15:00
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site to observe the contractor (CWM) and for the observation/testing of the placement of asphalt. The contractors began milling/paving hangar J and Lane #4 of the taxiway. Tack and fabric were placed along the taxiway over the existing asphalt. Tack and fabric were **not** placed in-between the hangars because after milling there was very little to no preexisting asphalt left. Density testing was performed and test results were compared with/provided to UES and CWM. A copy of the testing sheet will be provided in the pictures below. CWM increased the roll pattern with the rubber tire to help seal any minor cracking in the asphalt. This appears to help heal the cracking that is present.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

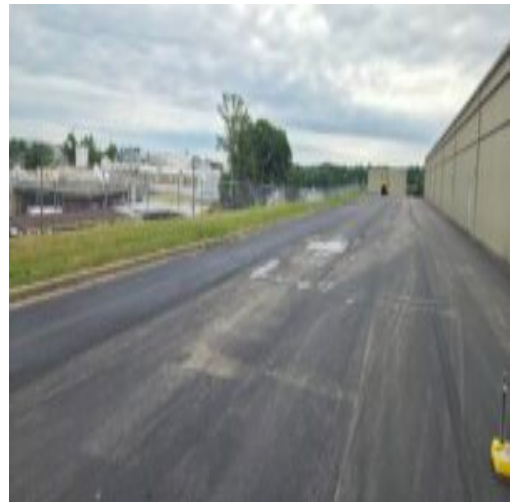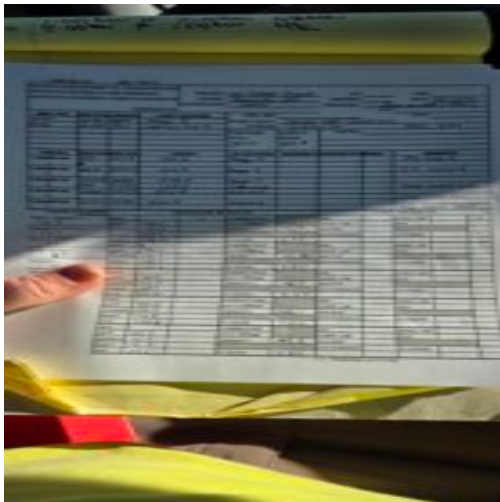

Date : 05/12/2026
Project No : 2025C187
Client Company : CWM
Arrival Time : 05/12/2026 10:00
Onsite Hours : 05:00

ASEC Report ID : 94331
Name of the Project : Lee Gilmer Memorial Airport - Rehab
Terminal Area Apron PH 3
Project Location : Gainesville
Weather : Sunny
Departure Time : 05/12/2026 15:00
ASEC Technician Name : Sean Willett



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
